Klassen corporation

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
Health Science Building		1041	01-Jul-08 A	01-Aug-12
Procurement Phase		469	01-Jul-08 A	07-May-10
CM Bidding Services		171	06-Apr-09 A	07-May-10
2500	DSA Approval	1	06-Apr-09 A	13-Oct-09 A
2270	Bid Package Preparation	20	14-Sep-09 A	19-Jan-10 A
2250	Prepare Construction Schedule	15	05-Oct-09 A	26-Jan-10
2510	Chancellor's Office Review	10	26-Oct-09 A	16-Dec-09 A
6560	Notice from Chancellor to go to bid	1	16-Dec-09 A	16-Dec-09 A
2280	Develop Bidders List	5	18-Jan-10 A	22-Jan-10
2290	Bidding / Clarifications / Addenda	41	18-Jan-10 A	17-Mar-10
2260	Establish Jobsite Logistics Plan	1	20-Jan-10	20-Jan-10
2200	Develop Bidders List	2	20-Jan-10	21-Jan-10
2210	Invitation and Instruction to Bidders	1	22-Jan-10	22-Jan-10
2350	Bid Documents Register / Distribution	30	25-Jan-10	05-Mar-10
2300	Pre-Bid Conferences	1	09-Feb-10*	09-Feb-10
2310	Bid Openings	1	18-Mar-10	18-Mar-10
2320	Bid Review / Pre-Award Conferences	4	18-Mar-10	23-Mar-10
2220	Prepare Contracts	10	19-Mar-10	01-Apr-10
2330	Recommend Award of Contracts	0		23-Mar-10
2340	Prepare Cash Flow Projections	5	24-Mar-10	30-Mar-10
2600	AVC Board of Trustees Meeting (Special Meeting)	0	29-Mar-10*	
2240	Accounting Set-Up	5	02-Apr-10	08-Apr-10
2230	Contractors Contract Compliance	25	02-Apr-10	06-May-10
2950	NTP (BP's 3005, 3021, 3041, 3072, 3075, 3195, 3351, 3367)	0	26-Apr-10	
2560	NTP Remaining Contracts	0	07-May-10	
Owner Procurement Services		451	01-Jul-08 A	12-Apr-10
2770	Authorization to Bid - Chancellors Office	1	01-Jul-08 A	01-Jul-08 A
2460	Authorization to Bid - AVC Board	1	14-Dec-09 A	14-Dec-09 A
2390	Prepare / Place Advertisement for Bid	1	23-Jan-10 A	23-Jan-10 A
2400	Attend Pre Bid Meetings	1	09-Feb-10	09-Feb-10
2410	Attend Bid Openings	1	18-Mar-10	18-Mar-10
2420	AVC FP&P Send Bid Recommendations To Chancellors Office	1	23-Mar-10	23-Mar-10
2120	Chancellors Office Authorizes Construction	14	24-Mar-10	12-Apr-10
2780	AVC Board Approval	1	29-Mar-10*	29-Mar-10
Submittals		110	26-Apr-10	29-Sep-10
CM Construction Services		110	26-Apr-10	29-Sep-10
6680	Underground Utilities	10	26-Apr-10	07-May-10
6800	Steel Decking	15	26-Apr-10	14-May-10
2880	Foundation Reinforcement Shop Drawings	15	26-Apr-10	14-May-10
2800	Fire Sprinkler Coordination Drawings (CADD)	20	26-Apr-10	21-May-10
6620	Elevators	40	26-Apr-10	21-Jun-10
6630	GFRC Paneling (AVC Approval Required)	40	26-Apr-10	21-Jun-10
6640	Fire Sprinklers	40	26-Apr-10	21-Jun-10
6580	Steel East Wing	80	26-Apr-10	17-Aug-10
6730	Section 08410 Aluminum Framed Storefronts	80	26-Apr-10	17-Aug-10
6850	Section 08900 Exterior Glazed Assemblies	80	26-Apr-10	17-Aug-10
2890	Four Pipe System	15	07-May-10	27-May-10
6700	Food Service Equipment (District approval needed)	20	07-May-10	04-Jun-10
6720	Metal Panels	20	07-May-10	04-Jun-10
6870	Lab Fixtures	20	07-May-10	04-Jun-10
6890	Plumbing Fixtures	20	07-May-10	04-Jun-10
6920	Fire Proofing	20	07-May-10	04-Jun-10
6940	Fume Hoods	20	07-May-10	04-Jun-10
8360	Access Control (AVC Approval Required)	20	07-May-10	04-Jun-10
2760	HVAC Coordination Drawings (CADD)	20	07-May-10	04-Jun-10
2790	Plumbing Coordination Drawings (CADD)	20	07-May-10	04-Jun-10
2810	Electrical,Fire Alarm, A/V Coordination Drawings (CADD)	20	07-May-10	04-Jun-10
2820	Communications Coordination Drawings (CADD)	20	07-May-10	04-Jun-10
6790	Handrailing	25	07-May-10	11-Jun-10
6820	Epoxy Terrazo	25	07-May-10	11-Jun-10
6830	Precast Terrazo Units	25	07-May-10	11-Jun-10
6840	ICU Sliding Doors	25	07-May-10	11-Jun-10
6710	Standing Seam Roofing	30	07-May-10	18-Jun-10
6740	Electrical Equipment	30	07-May-10	18-Jun-10
6760	Doors, Frames, and Hardware (AVC Approval Required)	30	07-May-10	18-Jun-10
6860	Fire Alarm	30	07-May-10	18-Jun-10
6880	Signage (district approval needed)	30	07-May-10	18-Jun-10
6900	HVAC Equipment (district approval needed)	30	07-May-10	18-Jun-10
6910	Audio Visual	30	07-May-10	18-Jun-10

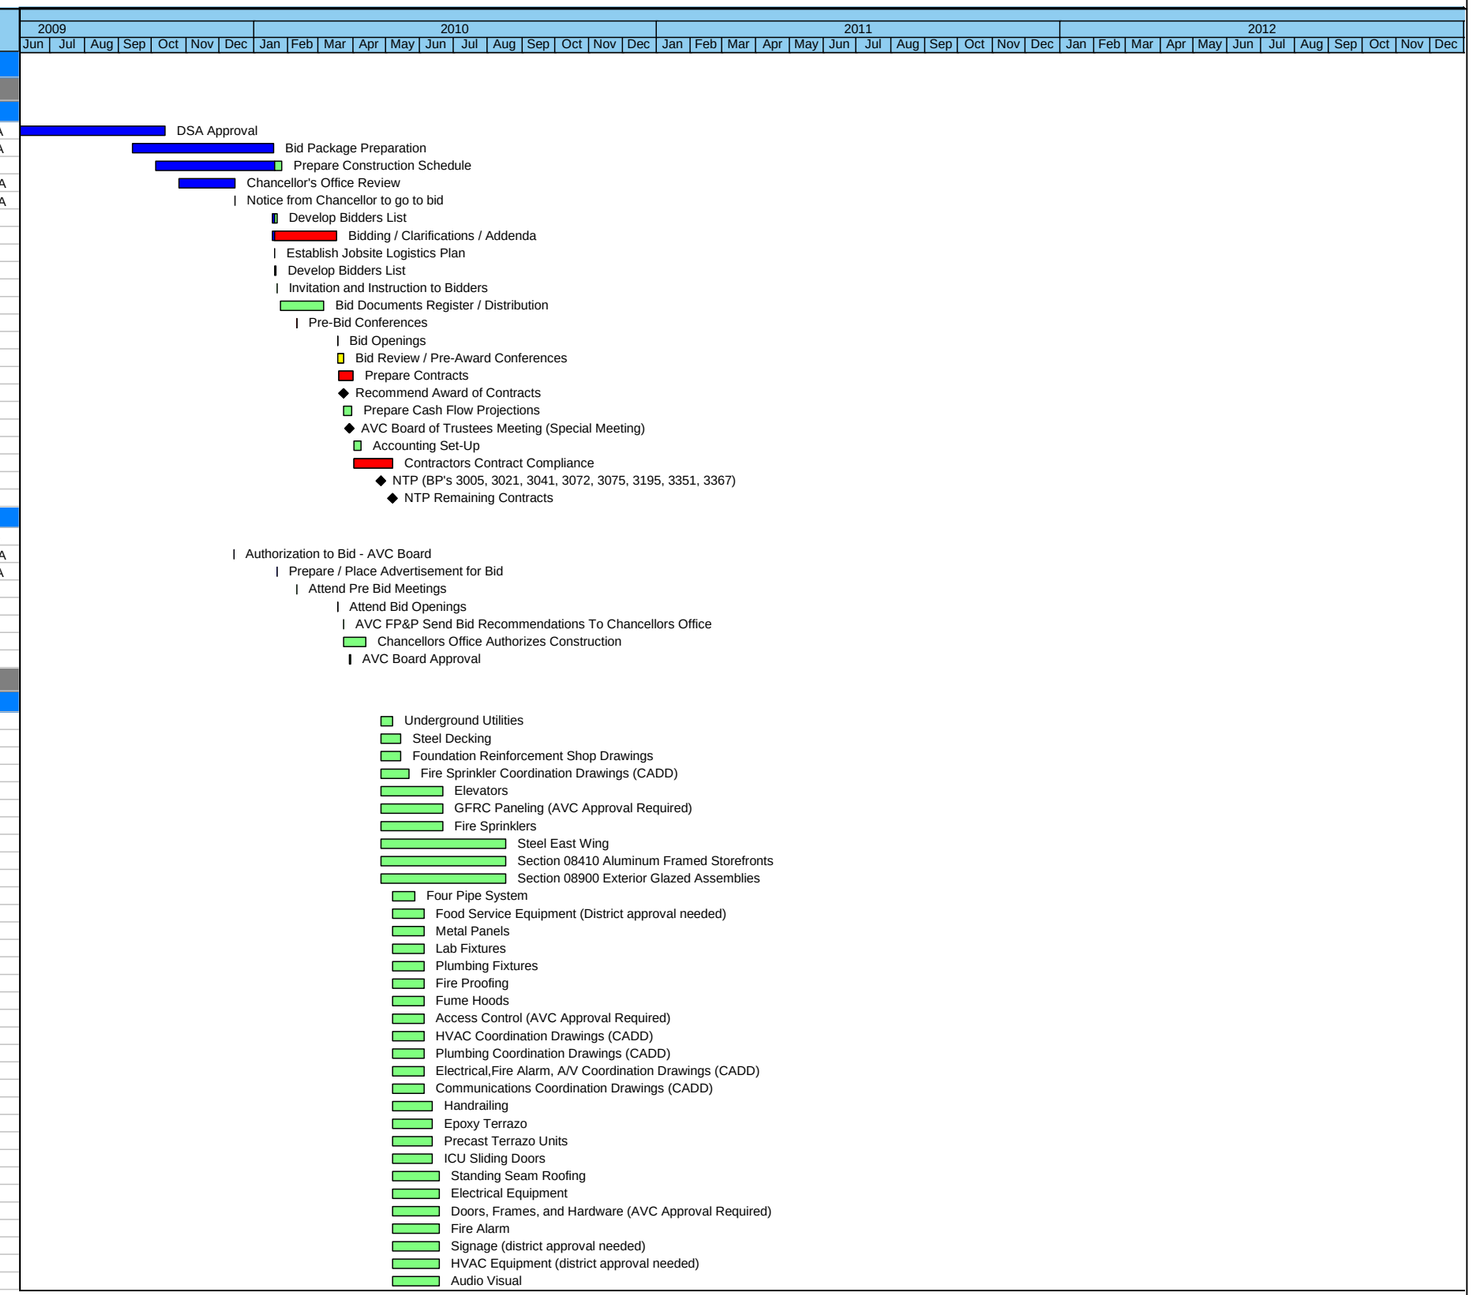

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
6930	Boilers	30	07-May-10	18-Jun-10
2870	Vinyl Fabric Wall Coverings (AVC Approval Required)	30	07-May-10	18-Jun-10
2490	Steel Foundation Embeds	35	07-May-10	25-Jun-10
6660	Lab Equipment	35	07-May-10	25-Jun-10
6810	Stainless Steel Work (district approval needed)	35	07-May-10	25-Jun-10
6650	Lab Casework (AVC Approval Required)	40	07-May-10	02-Jul-10
6690	Planetarium Seating (district approval needed)	40	07-May-10	02-Jul-10
6780	Greenhouse	40	07-May-10	02-Jul-10
6750	Planetarium Dome Screen Surface	60	07-May-10	02-Aug-10
6590	Steel North Wing	80	10-May-10	31-Aug-10
6600	Steel South Wing	80	24-May-10	15-Sep-10
6610	Steel Planetarium	80	08-Jun-10	29-Sep-10
2830	Final MEP Coordination Drawing Overlay	15	02-Jul-10	26-Jul-10
DSA Submittals		150	22-Jun-10	24-Jan-11
CM Construction Services		150	22-Jun-10	24-Jan-11
2480	Fire Sprinklers	110	22-Jun-10	24-Nov-10
6540	GFRC Paneling	110	22-Jun-10	24-Nov-10
6550	Elevators	110	22-Jun-10	24-Nov-10
6570	Curtain Wall Systems	110	18-Aug-10	24-Jan-11
Fabrication & Delivery		307	17-May-10	29-Jul-11
CM Construction Services		307	17-May-10	29-Jul-11
12780	Foundation Reinforcement	20	17-May-10	14-Jun-10
12850	Steel Decking	20	17-May-10	14-Jun-10
12820	Four Pipe System Piping	30	28-May-10	12-Jul-10
12840	Metal Panels	30	07-Jun-10	19-Jul-10
12600	ICU Sliding Door	40	14-Jun-10	09-Aug-10
12590	Door Frames	30	21-Jun-10	02-Aug-10
12540	HVAC Equipment	40	21-Jun-10	16-Aug-10
12620	Boilers	40	21-Jun-10	16-Aug-10
12550	Electrical Equipment	80	21-Jun-10	12-Oct-10
12390	Foundation Steel Embeds	15	28-Jun-10	19-Jul-10
12910	Stainless Steel Items	25	28-Jun-10	02-Aug-10
12580	Greenhouse	30	06-Jul-10	16-Aug-10
12610	Planetarium Seating	30	06-Jul-10	16-Aug-10
12630	Planetarium Dome Screen Surface	50	03-Aug-10	12-Oct-10
12400	Steel East Wing	50	18-Aug-10	27-Oct-10
12480	Section 08410 Aluminum Framed Storefronts	50	18-Aug-10	27-Oct-10
12410	Steel North Wing	50	02-Sep-10	10-Nov-10
12420	Steel South Wing	50	16-Sep-10	24-Nov-10
12430	Steel Planetarium	50	30-Sep-10	09-Dec-10
12440	GFRC Paneling System	30	26-Nov-10	10-Jan-11
12450	Elevators	60	26-Nov-10	21-Feb-11
12650	Stair # 2 Handrailing	25	18-Jan-11	22-Feb-11
12500	Section 08900 Exterior Glazed Assemblies	50	25-Jan-11	04-Apr-11
12660	Stair # 3 Handrailing	25	02-Feb-11	09-Mar-11
12640	Stair # 1 Handrailing	25	09-Feb-11	16-Mar-11
12670	Stair # 4 Handrailing	25	09-Feb-11	16-Mar-11
12510	Casework North Wing 1st Floor	30	17-Feb-11	31-Mar-11
12520	Casework South Wing 1st Floor	30	17-Feb-11	31-Mar-11
12460	Casework East Wing 1st floor	45	17-Feb-11	21-Apr-11
12830	Standing Seam Roofing	25	22-Feb-11	29-Mar-11
12470	Casework East Wing 2nd floor	30	28-Feb-11	11-Apr-11
12870	Casework North Wing 2nd Floor	30	28-Feb-11	11-Apr-11
12880	Casework South Wing 2nd Floor	30	07-Mar-11	18-Apr-11
12570	Observation Deck Handrailing	25	02-May-11	07-Jun-11
12530	Casework Planetarium 1st Floor	30	26-May-11	11-Jul-11
12860	Casework Planetarium 2nd Floor	30	16-Jun-11	29-Jul-11
Quality Control		444	20-Jan-10	14-Oct-11
Coordination Meetings		444	20-Jan-10	14-Oct-11
8750	Installation Steel/GFRC/Storefront/Aluminum Panels/Metal Studs	5	20-Jan-10	26-Jan-10
8600	AVC Site Access (grading/demo)	2	27-Apr-10	28-Apr-10
15290	Plumbing, Electric, Concrete Underground	2	07-May-10	10-May-10
8670	ADA/Access Review	2	07-May-10	10-May-10
8690	Terrazzo Flooring	2	07-May-10	10-May-10
8480	Submittals Steel/GFRC/Storefront/Aluminum Panels/Metal Studs	10	07-May-10	20-May-10
8520	Electrical/ Low Voltage	10	07-May-10	20-May-10
8610	Construction Schedule	20	07-May-10	04-Jun-10
8420	Plumbing & HVAC 4 Pipe System	10	07-Jun-10	18-Jun-10
8580	AVC Food Service	10	07-Jun-10	18-Jun-10

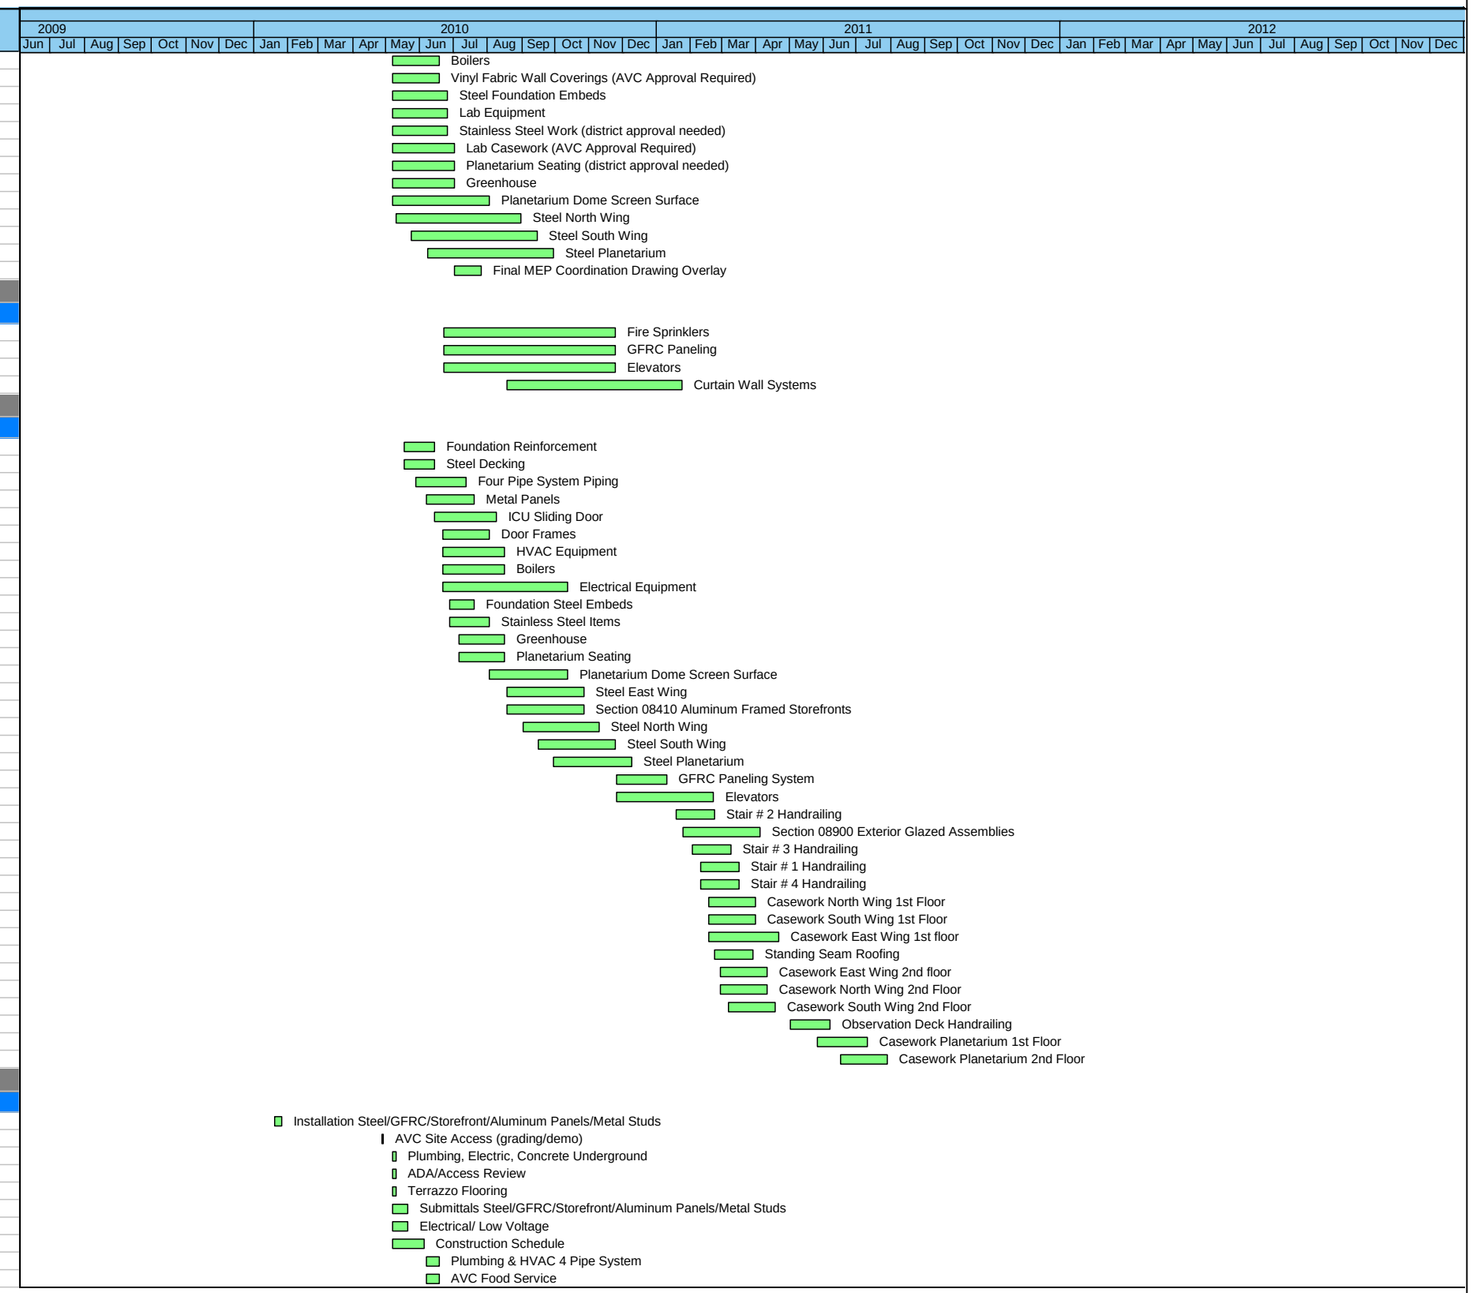

Actual Work | Near Critical | ◆ Milestone

Remaining Work | Critical Remaining Work

Klassen corporation

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
8430	MEP Above Ceiling	20	07-Jun-10	02-Jul-10
8700	Handrailing	2	14-Jun-10	15-Jun-10
8500	Doors/Metal Studs	2	21-Jun-10	22-Jun-10
8490	Electrical & Doors (Access Control)	10	21-Jun-10	02-Jul-10
8550	AVC Signage	10	21-Jun-10	02-Jul-10
8590	Food Service, Plumbing, Electric, HVAC	10	21-Jun-10	02-Jul-10
8620	AVC Final Color Selection Board	2	06-Jul-10	07-Jul-10
8660	Concrete/Seating	2	06-Jul-10	07-Jul-10
8680	Fire Alarm/Casework	2	06-Jul-10	07-Jul-10
8450	Casework/MEP	10	06-Jul-10	19-Jul-10
8560	AVC Doors, Hardware, Access Control	10	06-Jul-10	19-Jul-10
8640	Decking Penetrations	10	06-Jul-10	19-Jul-10
8470	Steel/Concrete at Foundations	5	20-Jul-10	26-Jul-10
8530	Elevator/Steel/Metal Studs/Drywall	2	29-Nov-10	30-Nov-10
8540	Elevator, Electric, Fire Alarm, Fire Sprinklers	2	29-Nov-10	30-Nov-10
8650	Elevator Pit	2	29-Nov-10	30-Nov-10
8440	Roof/Standing Seam/Metal Studs	2	02-Feb-11	03-Feb-11
8460	Backing	2	15-Feb-11	17-Feb-11
8510	Pre-Roofing Requirements (Metal Studs, Rough Carpentry, Roofing)	2	28-Mar-11	29-Mar-11
8630	Electrical Shutdown	2	14-Jul-11	15-Jul-11
8570	AVC Communications/ IT/ Audio Visual	10	03-Oct-11	14-Oct-11
Site Construction		578	26-Apr-10	27-Jul-12
CM Construction Services		578	26-Apr-10	27-Jul-12
2520	Job Kickoff Meeting	1	26-Apr-10	26-Apr-10
11910	Patch of Travel Access for campus	3	27-Apr-10	29-Apr-10
2580	Setup Jobsite and Staging area for construction	5	27-Apr-10	03-May-10
11600	Coordination Meeting for Demo, Electrical, undeground utilities, concrete...	3	04-May-10	06-May-10
11650	SWPPP Maintenance	2	07-May-10	10-May-10
11610	Electrical and Communications Shutdown	3	07-May-10	11-May-10
11620	Site Demolition in order to maintain campus access	20	12-May-10	09-Jun-10
11630	Rough Grading in order to start Construction	7	10-Jun-10	18-Jun-10
11640	Building Pad	7	21-Jun-10	29-Jun-10
11660	Storm Drain System to five feet outside building	15	30-Jun-10	21-Jul-10
11670	Sewer/waste Systems to five feet outside building	10	22-Jul-10	04-Aug-10
11700	Fireline to five feet outside building	3	05-Aug-10	09-Aug-10
13760	Four Pipe System Into Building	5	05-Aug-10	11-Aug-10
13700	Electrical Underground Duct Banks to Electrical Room	6	05-Aug-10	12-Aug-10
2670	Fire Line Shutdown/ Tie-in to Service	1	10-Aug-10	10-Aug-10
11690	Gas to five feet outside buildings	3	10-Aug-10	12-Aug-10
2740	Gas Shutdown/ Tie-in to Service	1	13-Aug-10	13-Aug-10
11680	Domestic Water to five feet outside buildings	5	13-Aug-10	19-Aug-10
2680	Domestic Water Shutdown/ Tie-in to Service	1	20-Aug-10	20-Aug-10
2685	Final Conduit/Ductbanks to Electrical Equipment	3	11-Jul-11	13-Jul-11
2695	Electrical Pads	3	14-Jul-11	18-Jul-11
2705	CMU wall Footings	4	14-Jul-11	19-Jul-11
2715	Set Electrical Equipment/Testing/Adjusting	5	19-Jul-11	25-Jul-11
2725	Feeders to equipment/building and testing	2	26-Jul-11	27-Jul-11
2735	Switch 13 Shutdown	1	28-Jul-11	28-Jul-11
2745	Final Electrical Equipment termination/startup/adjusting/testing	3	29-Jul-11	02-Aug-11
2755	CMU Wall	8	03-Aug-11	12-Aug-11
2765	Electrical Enclosure Gates	2	15-Aug-11	16-Aug-11
11760	Rough/Fine grade for Site work	7	07-Oct-11	17-Oct-11
11860	Excavate for Neutralization Tank	2	18-Oct-11	19-Oct-11
2775	Electrical To Site Lighting Bases	3	18-Oct-11	20-Oct-11
11850	Adjust utilities to final grades	5	18-Oct-11	24-Oct-11
11750	Irrigation System	7	18-Oct-11	26-Oct-11
11870	Neutralization Tank Slab	4	20-Oct-11	25-Oct-11
2785	Site Lighting Bases	4	21-Oct-11	26-Oct-11
11880	Neutralization Tank Walls/Top	8	26-Oct-11	04-Nov-11
11770	Center Courtyard and east side Soil amendments	5	27-Oct-11	02-Nov-11
11840	Centercourtyard and east side site electrical lighting work	10	27-Oct-11	09-Nov-11
11780	Center Courtyard and east side planter walls/curbs/mowstrips	15	03-Nov-11	28-Nov-11
11890	Curing walls/Waterproofing at Neutralization Tank	10	07-Nov-11	21-Nov-11
12300	North side Soil amendments	5	10-Nov-11	17-Nov-11
12360	South Side Soil amendments	5	18-Nov-11	28-Nov-11
11900	Backfill Neutralization Tank	1	22-Nov-11	22-Nov-11
12370	Grease Interceptor/ Neutralization tank work	10	23-Nov-11	08-Dec-11
11790	Center Courtyard and east side base material	2	29-Nov-11	30-Nov-11
13420	West side Soil amendments	5	29-Nov-11	05-Dec-11
12320	North Side planter walls/curbs/mowstrips	10	29-Nov-11	12-Dec-11

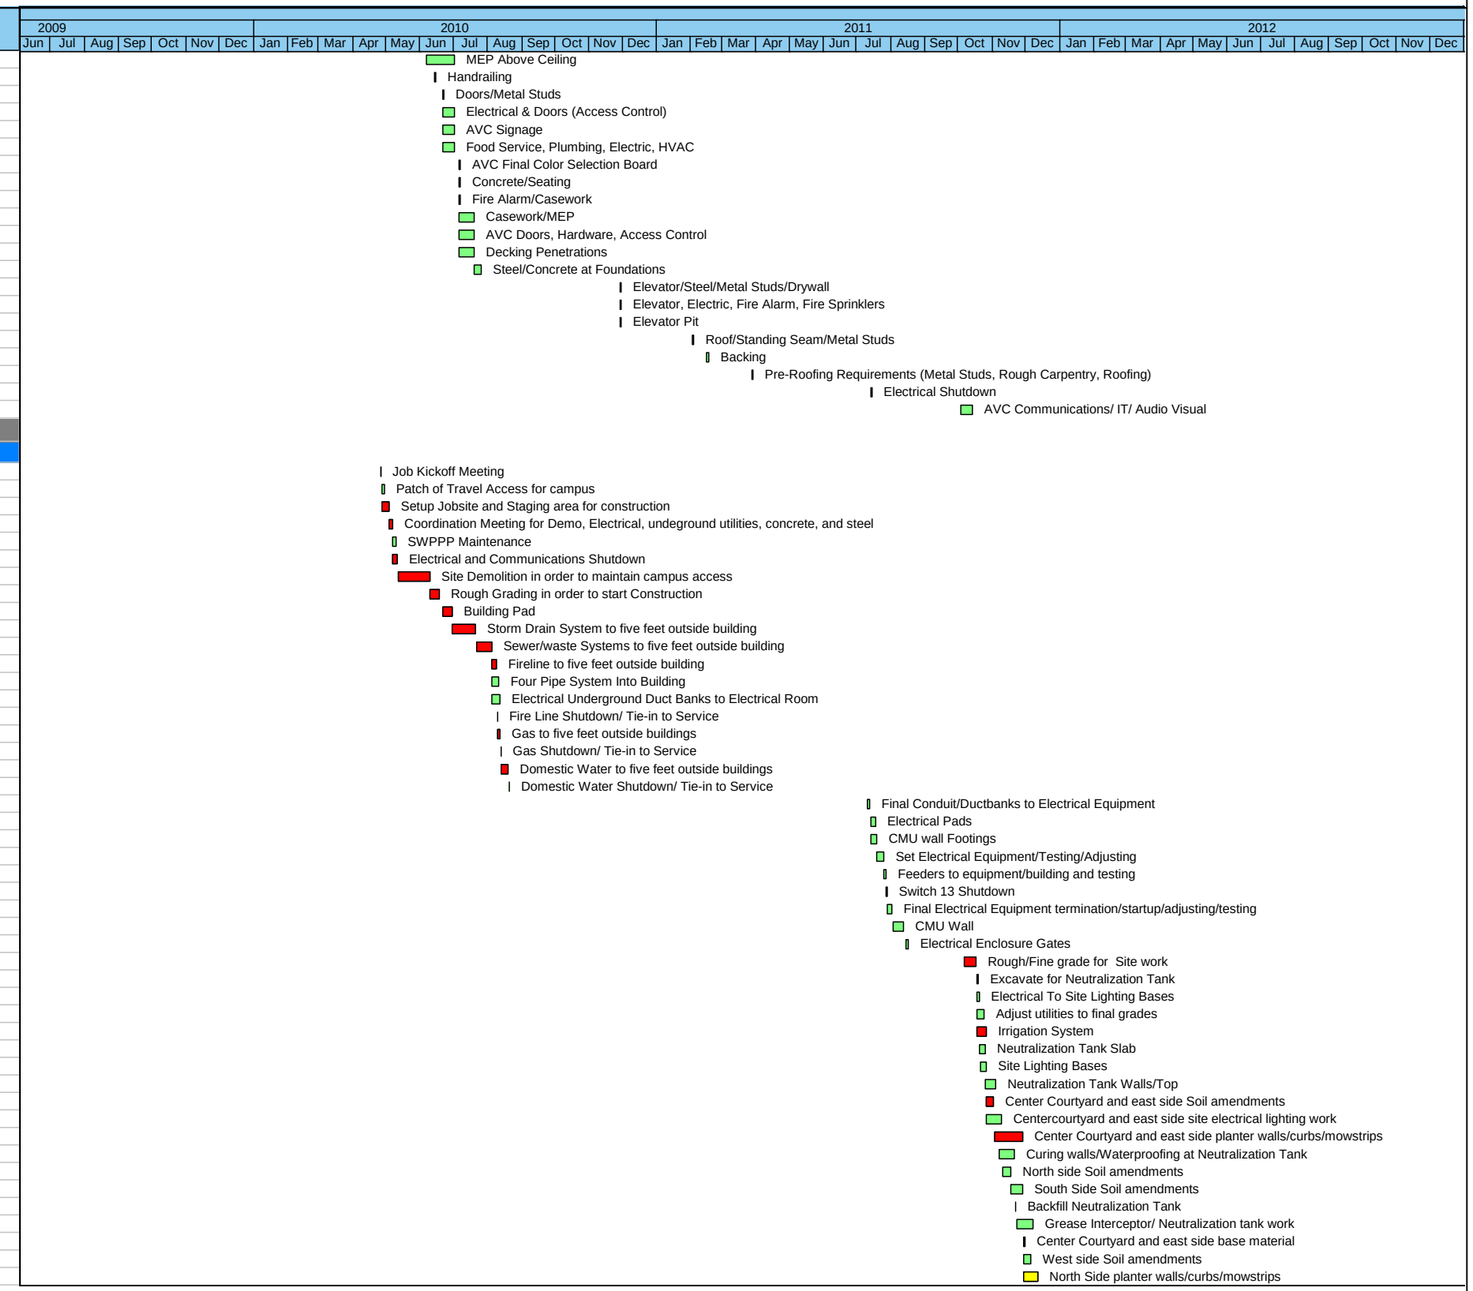

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
11800	Center Courtyard and east side flatwork	12	01-Dec-11	16-Dec-11
12330	North Side base material	2	13-Dec-11	14-Dec-11
12310	Set Lights in concrete at center courtyard	1	15-Dec-11	15-Dec-11
11810	Center Courtyard and east side Decomposed Granite	2	19-Dec-11	20-Dec-11
11820	Center Courtyard concrete pavers	3	19-Dec-11	21-Dec-11
12340	North Side flatwork	8	19-Dec-11	06-Jan-12
11830	Center Courtyard and east side landscaping	7	22-Dec-11	10-Jan-12
12350	North Side landscaping	7	09-Jan-12	17-Jan-12
12380	South Side planter walls/curbs/mowstrips	10	09-Jan-12	20-Jan-12
13400	South Side base material	2	23-Jan-12	24-Jan-12
13450	West Side planter walls/curbs/mowstrips	10	23-Jan-12	03-Feb-12
13410	South side flatwork	8	25-Jan-12	03-Feb-12
13430	South side Decomposed Granite	2	06-Feb-12	07-Feb-12
13470	West Side base material	2	06-Feb-12	07-Feb-12
13460	South landscaping	7	06-Feb-12	14-Feb-12
13480	West Side flatwork	8	08-Feb-12	17-Feb-12
13490	West Side landscaping	7	21-Feb-12	29-Feb-12
13650	Landscape Maintanence Period	90	22-Mar-12	27-Jul-12
APL Boiler Room		45	06-Jun-11	08-Aug-11
CM Construction Services		45	06-Jun-11	08-Aug-11
7810	Disconnect Work	2	06-Jun-11*	07-Jun-11
7800	Demolition	5	08-Jun-11	14-Jun-11
7790	Rough in Work prior to setting equipment	3	15-Jun-11	17-Jun-11
7780	Concrete Pads/curing	10	20-Jun-11	01-Jul-11
7770	Equipment	5	05-Jul-11	11-Jul-11
7760	Rough In work after setting equipment	10	12-Jul-11	25-Jul-11
7750	Finish Electrical,Plumbing, and Mechanical	7	26-Jul-11	03-Aug-11
7740	Doors / Louvers	2	04-Aug-11	05-Aug-11
7730	Startup,testing, commissioning	1	08-Aug-11	08-Aug-11
Green House		37	18-Oct-11	08-Dec-11
CM Construction Services		37	18-Oct-11	08-Dec-11
15150	Grading	2	18-Oct-11	19-Oct-11
7690	Electrical and Site Utilties to five feet outside of building	2	20-Oct-11	21-Oct-11
14610	Excavate Footings	1	24-Oct-11	24-Oct-11
10110	Plumbing under slab	2	25-Oct-11	26-Oct-11
11740	Electrical under slab	1	27-Oct-11	27-Oct-11
14650	Footing reinforcement/set posts	1	28-Oct-11	28-Oct-11
14670	Pour Footings	1	31-Oct-11	31-Oct-11
15140	Form Slab	1	01-Nov-11	01-Nov-11
15160	Slab Reinforcement	1	02-Nov-11	02-Nov-11
15180	Slab utilities	2	03-Nov-11	04-Nov-11
15170	Pour Slab /Strip/ Cleanup	2	07-Nov-11	08-Nov-11
15200	Green House	10	09-Nov-11	23-Nov-11
15210	Green House Utilities	4	28-Nov-11	01-Dec-11
15220	Green House Benches	2	02-Dec-11	05-Dec-11
15230	Finish Utilities	3	06-Dec-11	08-Dec-11
Building Construction		368	20-Aug-10	31-Jan-12
Structure		310	20-Aug-10	07-Nov-11
Foundation		192	20-Aug-10	20-May-11
East Wing		115	20-Aug-10	02-Feb-11
2720	Building Plumbing Underground	5	20-Aug-10	26-Aug-10
5960	Building Electrical Underground	5	27-Aug-10	02-Sep-10
5970	Excavate / Form Footings / Pits	4	11-Oct-10	14-Oct-10
5980	Footing / Pit Slab Reinforcement / Baseplates	8	15-Oct-10	26-Oct-10
5990	Pour / Strip / Clean Footings / Pit slab	3	29-Oct-10	02-Nov-10
6000	Underslab Electrical	5	03-Nov-10	09-Nov-10
6080	Form Pit Walls	5	03-Nov-10	09-Nov-10
6090	Reinforcement at Pit Walls	3	10-Nov-10	15-Nov-10
6010	Underslab Plumbing	10	10-Nov-10	24-Nov-10
6100	Pour/strip/clean Pit Walls	3	16-Nov-10	18-Nov-10
8770	Pit Waterproofing/cure	7	18-Nov-10	26-Nov-10
6020	Vapor Barrier/Sand/gravel	2	29-Nov-10	30-Nov-10
6110	Backfill Pit Walls	2	29-Nov-10	30-Nov-10
6030	Form Slab & Block out columns/frames	3	01-Dec-10	03-Dec-10
6040	Slab Reinforcement	2	06-Dec-10	07-Dec-10
6050	Pour Slab/Cleanup	2	08-Dec-10	09-Dec-10
6060	Form/Reinforcement Curbs/Equipment Pads	3	10-Dec-10	14-Dec-10
6130	Structural Steel	15	10-Dec-10	10-Jan-11
6070	Pour/strip/cleanup curbs	2	15-Dec-10	16-Dec-10

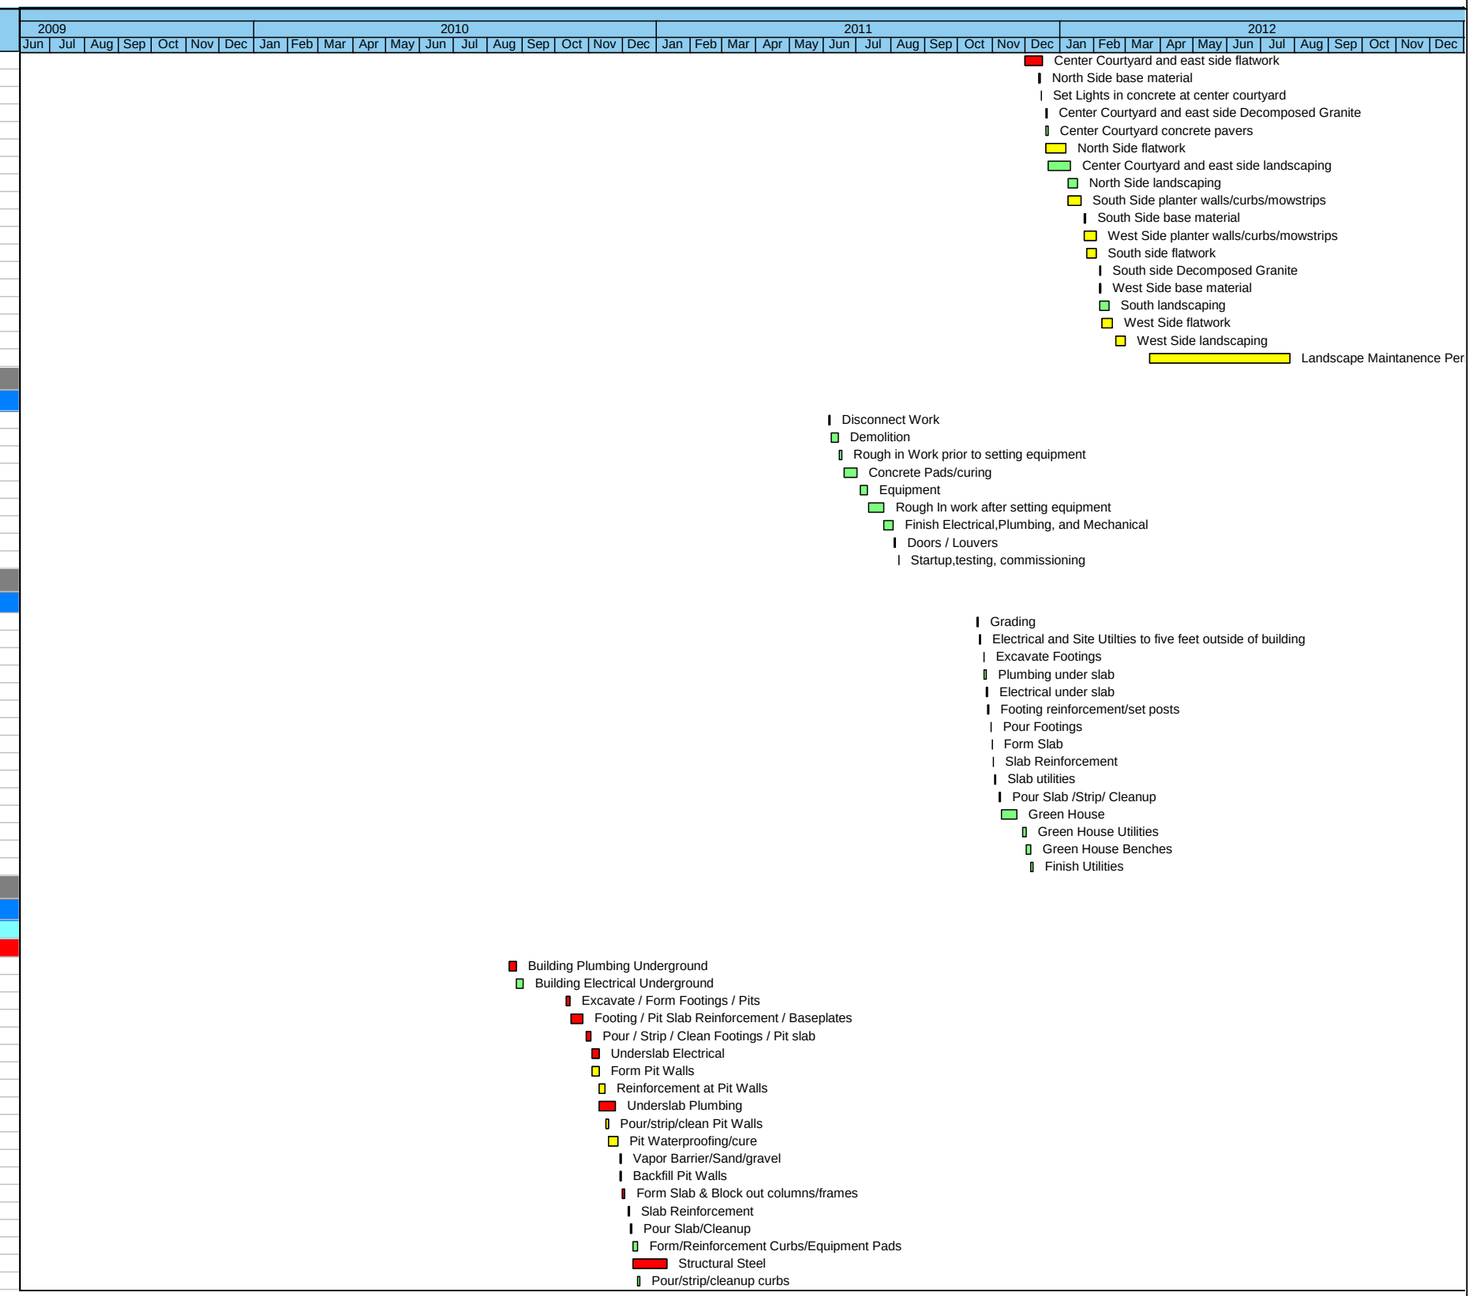

Actual Work | Near Critical | ◆ Milestone

Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
6140	Steel Decking	5	22-Dec-10	06-Jan-11
6150	Steel Decking HVAC Penetrations / Underslab	3	07-Jan-11	11-Jan-11
6440	Steel Decking Electrical Penetrations / Underslab	3	07-Jan-11	11-Jan-11
6460	Steel Decking Plumbing Penetrations / Underslab	3	07-Jan-11	11-Jan-11
6220	Stair Framing	7	11-Jan-11	19-Jan-11
6160	2nd Floor Deck reinforcement	2	12-Jan-11	13-Jan-11
6170	2nd Floor Deck Pour/cleanup	2	14-Jan-11	17-Jan-11
6180	Roof Steel Decking	4	18-Jan-11	21-Jan-11
6230	Stair Step Infill	2	20-Jan-11	21-Jan-11
6190	Roof Decking HVAC Penetrations / Underslab	3	24-Jan-11	26-Jan-11
6450	Roof Decking Electrical Penetrations / Underslab	3	24-Jan-11	26-Jan-11
6470	Roof Decking Plumbing Penetrations / Underslab	3	24-Jan-11	26-Jan-11
6200	Roof Decking Reinforcement	2	27-Jan-11	28-Jan-11
6210	Roof Decking Pour/ Cleanup	2	31-Jan-11	01-Feb-11
6770	Stair Field Measurements	1	02-Feb-11	02-Feb-11
North Wing		109	27-Aug-10	01-Feb-11
3680	Building Plumbing Underground	15	27-Aug-10	17-Sep-10
6240	Building Electrical Underground	5	20-Sep-10	24-Sep-10
6960	Excavate/Form Footings/Pits	4	11-Oct-10	14-Oct-10
6970	Footing/Pit Slab Reinforcement/Baseplates	8	15-Oct-10	26-Oct-10
6980	Pour/Strip/Clean Footings/Pit slab	3	29-Oct-10	02-Nov-10
7000	Form Pit Walls	2	03-Nov-10	04-Nov-10
6990	Underslab Electrical	5	03-Nov-10	09-Nov-10
7010	Reinforcement at Pit Walls	2	05-Nov-10	08-Nov-10
7020	Pour/strip/clean Pit Walls	3	09-Nov-10	12-Nov-10
7040	Underslab Plumbing	10	10-Nov-10	24-Nov-10
8780	Pit Waterproofing/cure	7	12-Nov-10	19-Nov-10
7030	Backfill Pit Walls	2	22-Nov-10	23-Nov-10
7050	Vapor Barrier/Sand/gravel	2	29-Nov-10	30-Nov-10
7060	Form Slab & Block out columns/frames	3	01-Dec-10	03-Dec-10
7070	Slab Reinforcement	2	06-Dec-10	07-Dec-10
7080	Pour Slab/Cleanup	2	08-Dec-10	09-Dec-10
7090	Form/Reinforcement @ Curbs/Equipment Pads	3	10-Dec-10	14-Dec-10
7100	Structural Steel	15	10-Dec-10	10-Jan-11
7110	Pour/strip/cleanup curbs	2	15-Dec-10	16-Dec-10
7120	Steel Decking	5	22-Dec-10	06-Jan-11
7140	Steel Decking HVAC Penetrations / Underslab	3	07-Jan-11	11-Jan-11
7700	Steel Decking Electrical Penetrations / Underslab	3	07-Jan-11	11-Jan-11
7720	Steel Decking Plumbing Penetrations / Underslab	3	07-Jan-11	11-Jan-11
7130	Stair Framing	7	11-Jan-11	19-Jan-11
7160	2nd Floor Deck reinforcement	2	12-Jan-11	13-Jan-11
7170	2nd Floor Deck Pour / Cleanup	2	14-Jan-11	17-Jan-11
3760	Stair Field Measurement	1	18-Jan-11	18-Jan-11
7180	Roof Steel Decking	4	18-Jan-11	21-Jan-11
7150	Stair Step Infill	1	20-Jan-11	20-Jan-11
7190	Roof Decking HVAC Penetrations / Underslab	3	24-Jan-11	26-Jan-11
7710	Roof Decking Electrical Penetrations / Underslab	3	24-Jan-11	26-Jan-11
7880	Roof Decking Plumbing Penetrations / Underslab	3	24-Jan-11	26-Jan-11
7200	Roof Decking Reinforcement	2	27-Jan-11	28-Jan-11
7210	Roof Decking Pour / Cleanup	2	31-Jan-11	01-Feb-11
South Wing		100	20-Sep-10	09-Feb-11
3720	Building Plumbing Underground	15	20-Sep-10	08-Oct-10
7220	Building Electrical Underground	5	11-Oct-10	15-Oct-10
7240	Excavate/Form Footings/Pits	4	18-Oct-10	21-Oct-10
7250	Footing/Pit Slab Reinforcement/Baseplates	8	22-Oct-10	02-Nov-10
7260	Pour/Strip/Clean Footings/Pit slab	3	05-Nov-10	09-Nov-10
7280	Form Pit Walls	2	10-Nov-10	12-Nov-10
7270	Underslab Electrical	5	10-Nov-10	17-Nov-10
7290	Reinforcement at Pit Walls	2	15-Nov-10	16-Nov-10
7300	Pour Pit Walls/Strip/Clean	2	17-Nov-10	18-Nov-10
7320	Underslab Plumbing	10	18-Nov-10	03-Dec-10
3780	Pit Waterproofing/Cure	7	18-Nov-10	26-Nov-10
7310	Backfill Pit Walls	2	29-Nov-10	30-Nov-10
7330	Vapor Barrier/Sand/gravel	2	06-Dec-10	07-Dec-10
7340	Form Slab & Block out columns/frames	3	08-Dec-10	10-Dec-10
7350	Slab Reinforcement	2	13-Dec-10	14-Dec-10
7360	Pour Slab/Cleanup	2	15-Dec-10	16-Dec-10
7370	Form/Reinforcement @ Curbs/Equipment Pads	3	17-Dec-10	21-Dec-10
7380	Structural Steel	15	17-Dec-10	17-Jan-11
7390	Pour/strip/cleanup curbs	2	22-Dec-10	03-Jan-11
7400	Steel Decking	5	07-Jan-11	13-Jan-11

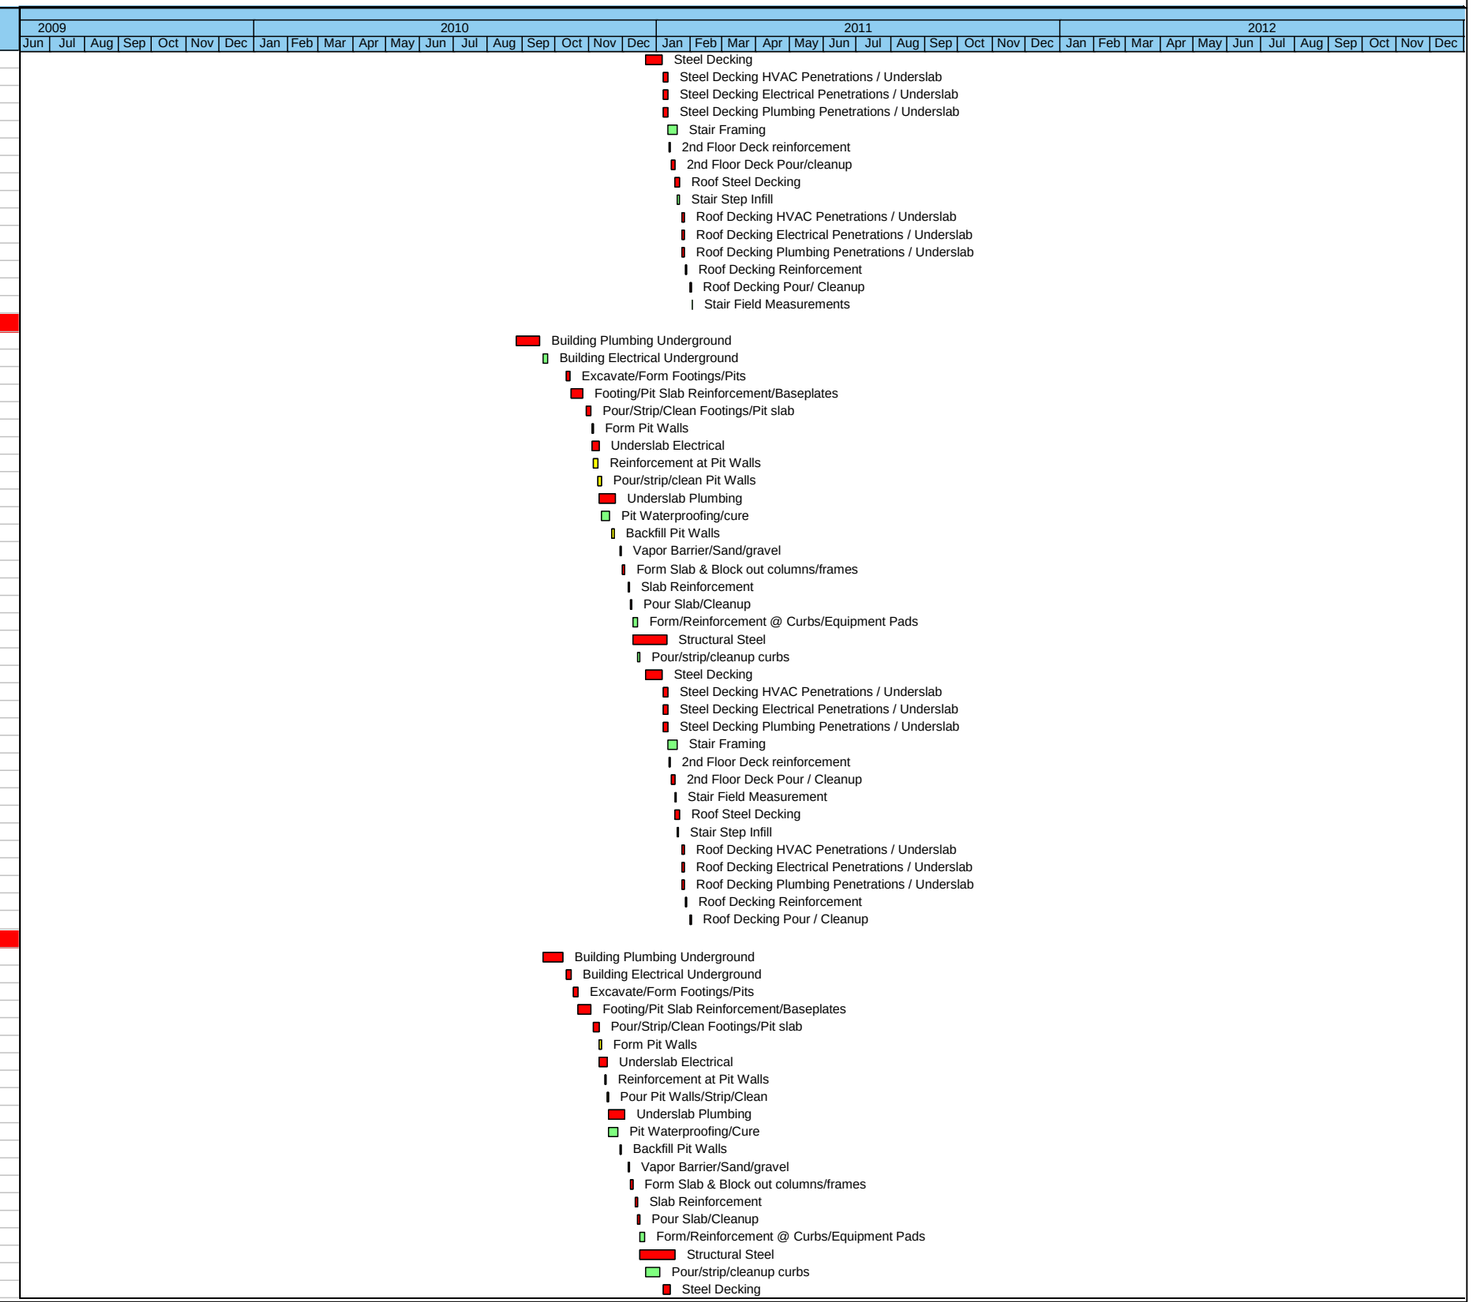

Actual Work
Remaining Work
Near Critical
Critical Remaining Work
◆ Milestone

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
7420	Steel Decking HVAC Penetrations / Underslab	3	14-Jan-11	18-Jan-11
7890	Steel Decking Electrical Penetrations / Underslab	3	14-Jan-11	18-Jan-11
7910	Steel Decking Plumbing Penetrations / Underslab	3	14-Jan-11	18-Jan-11
7410	Stair Framing	7	18-Jan-11	26-Jan-11
7440	2nd Floor Deck reinforcement	2	19-Jan-11	20-Jan-11
7450	2nd Floor Deck Pour/Cleanup	2	21-Jan-11	24-Jan-11
7460	Roof Steel Decking	4	25-Jan-11	28-Jan-11
7430	Stair Step Infill	2	27-Jan-11	28-Jan-11
7470	Roof Decking HVAC Penetrations / Underslab	3	31-Jan-11	02-Feb-11
7900	Roof Decking Electrical Penetrations / Underslab	3	31-Jan-11	02-Feb-11
7920	Roof Decking Plumbing Penetrations / Underslab	3	31-Jan-11	02-Feb-11
7480	Roof Decking Reinforcement	2	03-Feb-11	04-Feb-11
7490	Roof Decking Pour/Cleanup	2	07-Feb-11	08-Feb-11
3770	Stair Field Measurement	1	09-Feb-11	09-Feb-11
Planetarium		89	18-Jan-11	20-May-11
5090	Plumbing Underground	8	18-Jan-11	27-Jan-11
5100	Electrical Underground	5	28-Jan-11	03-Feb-11
2570	Excavate Footings	3	04-Feb-11	08-Feb-11
5110	Footing reinforcement/embeds	5	09-Feb-11	15-Feb-11
5120	Pour Footings/caissons/ strip/ clean	2	18-Feb-11	22-Feb-11
5130	Structural Steel	20	23-Feb-11	22-Mar-11
5140	Bond Beam forming/reinforcement	5	23-Mar-11	29-Mar-11
5150	Pour Moment Frame Bond Beams/strip/clean	2	31-Mar-11	01-Apr-11
5160	Backfill	2	04-Apr-11	05-Apr-11
5170	Form slab	2	06-Apr-11	07-Apr-11
5180	Sand/gravel/vapor barrier at slab	1	08-Apr-11	08-Apr-11
5190	Slab reinforcement	2	11-Apr-11	12-Apr-11
5200	Pour Slab/ Cleanup	2	13-Apr-11	14-Apr-11
5210	2nd Floor Decking	5	15-Apr-11	21-Apr-11
5220	2nd Floor HVAC Penetrations / Underslab	4	22-Apr-11	27-Apr-11
6480	2nd Floor Electrical Penetrations / Underslab	4	22-Apr-11	27-Apr-11
6500	2nd Floor Plumbing Penetrations / Underslab	4	22-Apr-11	27-Apr-11
5230	2nd Floor Deck reinforcement/formwork	2	28-Apr-11	29-Apr-11
5240	Pour Second floor deck	1	02-May-11	02-May-11
8760	Stair Field Measurement	1	03-May-11	03-May-11
5250	Roof Decking	4	03-May-11	06-May-11
5260	HVAC Roof Penetrations / Underslab	5	09-May-11	13-May-11
6490	Electircal Systems Roof Penetrations / Underslab	5	09-May-11	13-May-11
6510	Plumbing Roof Penetrations / Underslab	5	09-May-11	13-May-11
5270	Roof formwork/reinforcement	3	16-May-11	18-May-11
5280	Pour Roof Deck/ Cleanup	2	19-May-11	20-May-11
Framing & Rough-In		120	18-Jan-11	06-Jul-11
East Wing		67	18-Jan-11	20-Apr-11
2710	Fireproofing	6	18-Jan-11	25-Jan-11
4810	Rough-in Coordination	25	18-Jan-11	22-Feb-11
4800	Metal Studs/ Blocking / Bracing	15	25-Jan-11	15-Feb-11
4900	Blocking/backing Review	2	15-Feb-11	17-Feb-11
4910	Initial Field Measurements @ Stud Finish	2	15-Feb-11	17-Feb-11
4890	Door Frames	3	15-Feb-11	18-Feb-11
4820	Plumbing Systems Rough In	10	15-Feb-11	02-Mar-11
4860	4 Pipe System Rough-In	10	15-Feb-11	02-Mar-11
4840	HVAC Rough In	10	02-Mar-11	16-Mar-11
4850	Electrical Systems Rough-In	10	16-Mar-11	30-Mar-11
8370	Communications Rough-In/Cable Management	10	16-Mar-11	30-Mar-11
4830	Fire Sprinkler Rough-in	15	16-Mar-11	06-Apr-11
4870	Testing of Rough-in Systems/record Drawings/Pictures	5	06-Apr-11	13-Apr-11
4880	Insulations/Firesafing	5	13-Apr-11	20-Apr-11
North Wing		72	18-Jan-11	27-Apr-11
3730	Fireproofing	6	18-Jan-11	25-Jan-11
4940	Rough-in Coordination	25	18-Jan-11	22-Feb-11
4950	Metal Studs/ Blocking / Bracing	15	25-Jan-11	15-Feb-11
4990	Blocking/backing Review	2	15-Feb-11	17-Feb-11
5000	Initial Field Measurements @ Stud Finish	2	15-Feb-11	17-Feb-11
4980	Door Frames	3	15-Feb-11	18-Feb-11
4970	4 Pipe System Rough-In	10	15-Feb-11	02-Mar-11
4960	Plumbing Systems Rough In	15	15-Feb-11	09-Mar-11
5020	HVAC Rough In	10	09-Mar-11	23-Mar-11
5030	Electrical Systems Rough-In	10	23-Mar-11	06-Apr-11
8380	Communications Rough-In / Cable Management	10	23-Mar-11	06-Apr-11
5010	Fire Sprinkler Rough-in	15	23-Mar-11	13-Apr-11
5040	Testing of Rough-in Systems/record Drawings/Pictures	5	13-Apr-11	20-Apr-11

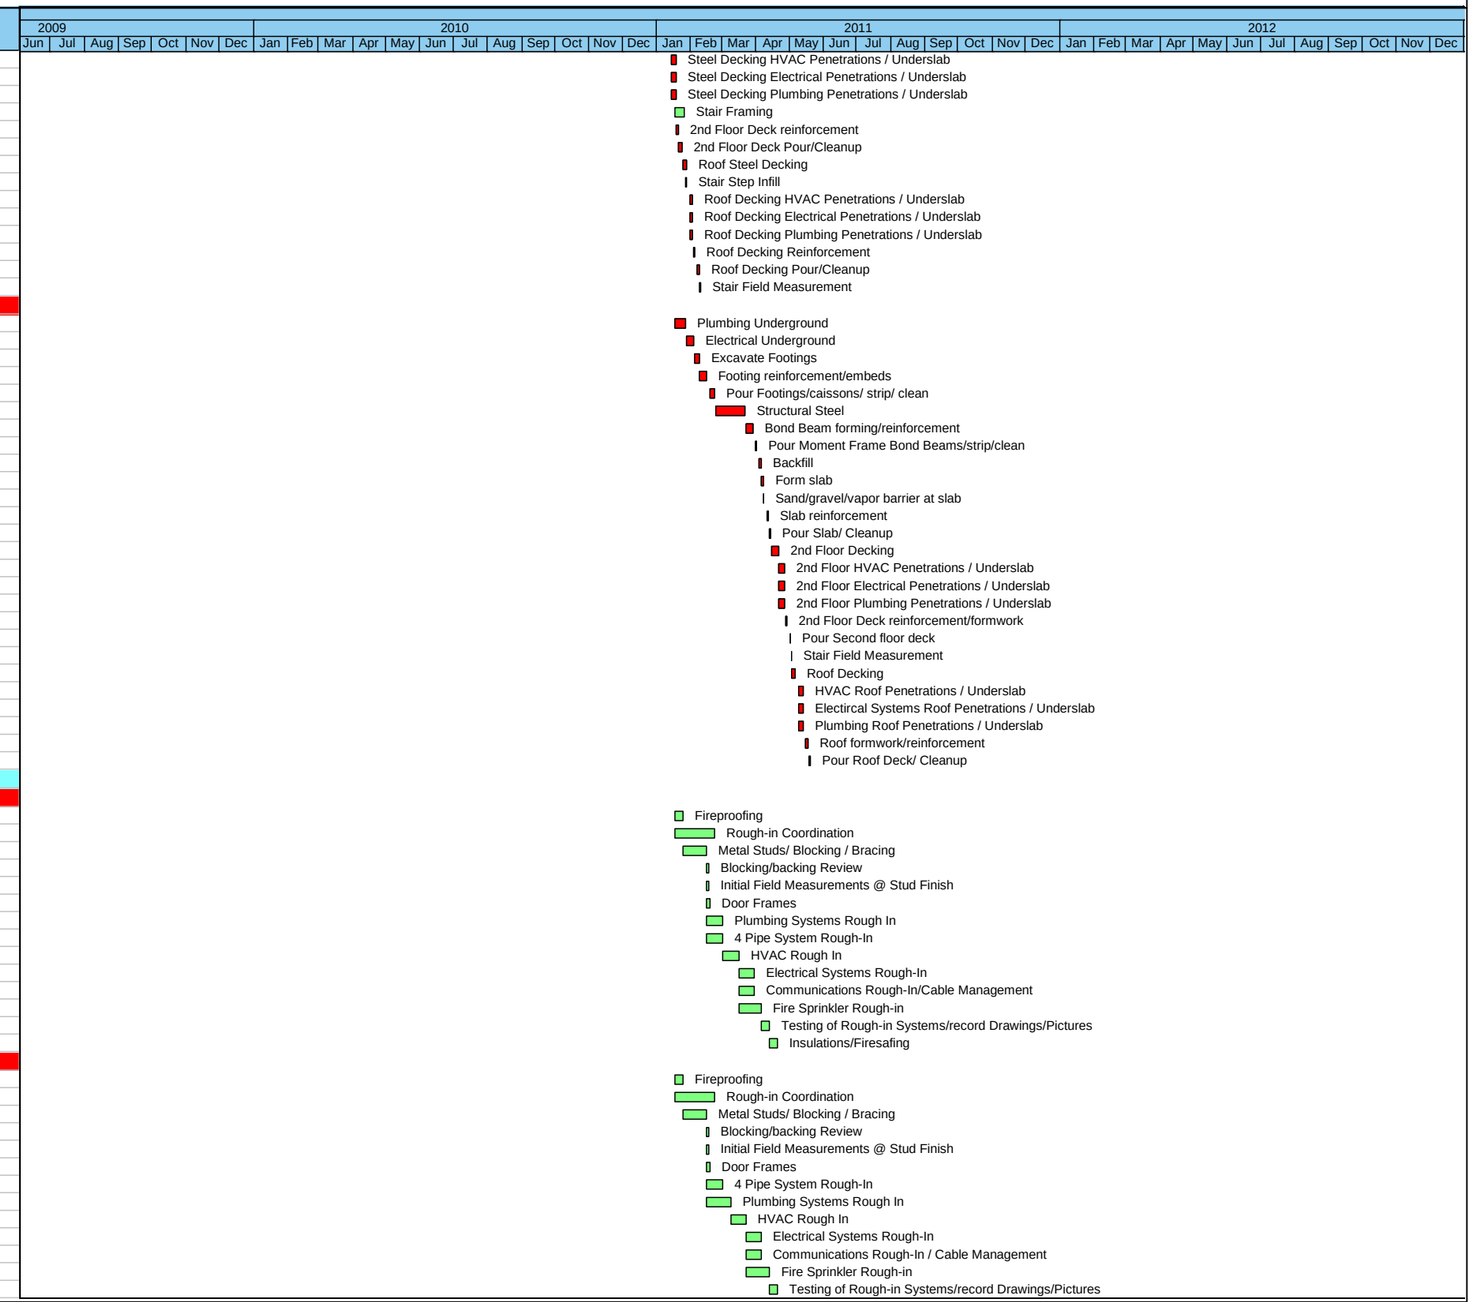

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
5050	Insulations/Firesafing	5	20-Apr-11	27-Apr-11
South Wing		57	25-Jan-11	13-Apr-11
5070	Fireproofing	6	25-Jan-11	01-Feb-11
5060	Rough-in Coordination	25	25-Jan-11	01-Mar-11
5080	Metal Studs/ Blocking / Bracing	10	01-Feb-11	15-Feb-11
5410	Blocking/backing Review	2	15-Feb-11	17-Feb-11
5420	Initial Field Measurements @ Stud Finish	2	15-Feb-11	17-Feb-11
5400	Door Frames	3	15-Feb-11	18-Feb-11
5380	Plumbing Systems Rough In	5	15-Feb-11	23-Feb-11
5390	4 Pipe System Rough-In	5	15-Feb-11	23-Feb-11
5440	HVAC Rough In	10	23-Feb-11	09-Mar-11
5450	Electrical Systems Rough-In	10	09-Mar-11	23-Mar-11
8390	Communications Rough-In / Cable Management	10	09-Mar-11	23-Mar-11
5430	Fire Sprinkler Rough-in	15	09-Mar-11	30-Mar-11
5460	Testing of Rough-in Systems/record Drawings/Pictures	5	30-Mar-11	06-Apr-11
5470	Insulations/Firesafing	5	06-Apr-11	13-Apr-11
Planetarium		45	03-May-11	06-Jul-11
5490	Fireproofing	6	03-May-11	10-May-11
5480	Rough-in Coordination	25	03-May-11	07-Jun-11
5500	Metal Studs/ Blocking / Bracing	10	10-May-11	24-May-11
5540	Blocking/backing Review	2	24-May-11	26-May-11
5550	Initial Field Measurements @ Stud Finish	2	24-May-11	26-May-11
5530	Door Frames	3	24-May-11	27-May-11
5510	Plumbing Systems Rough In	5	24-May-11	01-Jun-11
5520	4 Pipe System Rough-In	5	24-May-11	01-Jun-11
5570	HVAC Rough In	7	01-Jun-11	10-Jun-11
5560	Fire Sprinkler Rough-in	7	10-Jun-11	21-Jun-11
5580	Electrical Systems Rough-In	7	10-Jun-11	21-Jun-11
8400	Communications Rough-In/Cable Management	10	10-Jun-11	24-Jun-11
5590	Testing of Rough-in Systems/record Drawings/Pictures	5	21-Jun-11	28-Jun-11
5600	Insulations/Firesafing	5	28-Jun-11	06-Jul-11
Framing & Rough-In 2nd Floor		134	02-Feb-11	10-Aug-11
East Wing		54	02-Feb-11	18-Apr-11
5290	Elevator # 3 Shaft Wall Framing	5	02-Feb-11	08-Feb-11
5950	Fireproofing	6	02-Feb-11	09-Feb-11
7510	Rough-in Coordination	25	02-Feb-11	09-Mar-11
5300	Elevator # 3 Rough In	3	09-Feb-11	11-Feb-11
7500	Metal Studs/ Blocking / Bracing	10	09-Feb-11	24-Feb-11
5310	Elevator # 3 Drywall	3	14-Feb-11	16-Feb-11
5350	Elevator # 3 Pit Ladder	1	17-Feb-11	17-Feb-11
5340	Elevator # 3 Finish Utilities	3	18-Feb-11	23-Feb-11
5320	Elevator # 3 Installation	10	24-Feb-11	09-Mar-11
7600	Blocking/backing Review	2	24-Feb-11	28-Feb-11
7610	Initial Field Measurements @ Stud Finish	2	24-Feb-11	28-Feb-11
7590	Door Frames	3	24-Feb-11	01-Mar-11
7560	4 Pipe System Rough-In	5	24-Feb-11	03-Mar-11
7520	Plumbing Systems Rough In	10	24-Feb-11	10-Mar-11
5330	Elevator # 3 Corrections for Final Inspection	5	10-Mar-11	16-Mar-11
7540	HVAC Rough In	7	10-Mar-11	21-Mar-11
7530	Fire Sprinkler Rough-in	7	21-Mar-11	30-Mar-11
7550	Electrical Systems Rough-In	10	21-Mar-11	04-Apr-11
8410	Communications Rough-In/Cable Management	10	21-Mar-11	04-Apr-11
7570	Testing of Rough-in Systems/record Drawings/Pictures	5	04-Apr-11	11-Apr-11
7580	Insulations/Firesafing	5	11-Apr-11	18-Apr-11
North Wing		54	02-Feb-11	18-Apr-11
5360	Elevator # 2 Shaft Wall Framing	5	02-Feb-11	08-Feb-11
16030	Fireproofing	6	02-Feb-11	09-Feb-11
16050	Rough-in Coordination	25	02-Feb-11	09-Mar-11
5370	Elevator # 2 Rough In	3	09-Feb-11	11-Feb-11
16040	Metal Studs/ Blocking / Bracing	10	09-Feb-11	24-Feb-11
5670	Elevator # 2 Drywall	3	14-Feb-11	16-Feb-11
6250	Elevator # 2 Pit Ladder	1	17-Feb-11	17-Feb-11
8260	Elevator # 2 Finish Utilities	3	18-Feb-11	23-Feb-11
8270	Elevator # 2 Installation	10	24-Feb-11	09-Mar-11
16130	Door Frames	2	24-Feb-11	28-Feb-11
16140	Blocking/backing Review	2	24-Feb-11	28-Feb-11
16150	Initial Field Measurements @ Stud Finish	2	24-Feb-11	28-Feb-11
16100	4 Pipe System Rough-In	5	24-Feb-11	03-Mar-11
16060	Plumbing Systems Rough In	10	24-Feb-11	10-Mar-11
16080	HVAC Rough In	7	10-Mar-11	21-Mar-11
8280	Elevator # 2 Corrections for Final Inspection	5	18-Mar-11	24-Mar-11

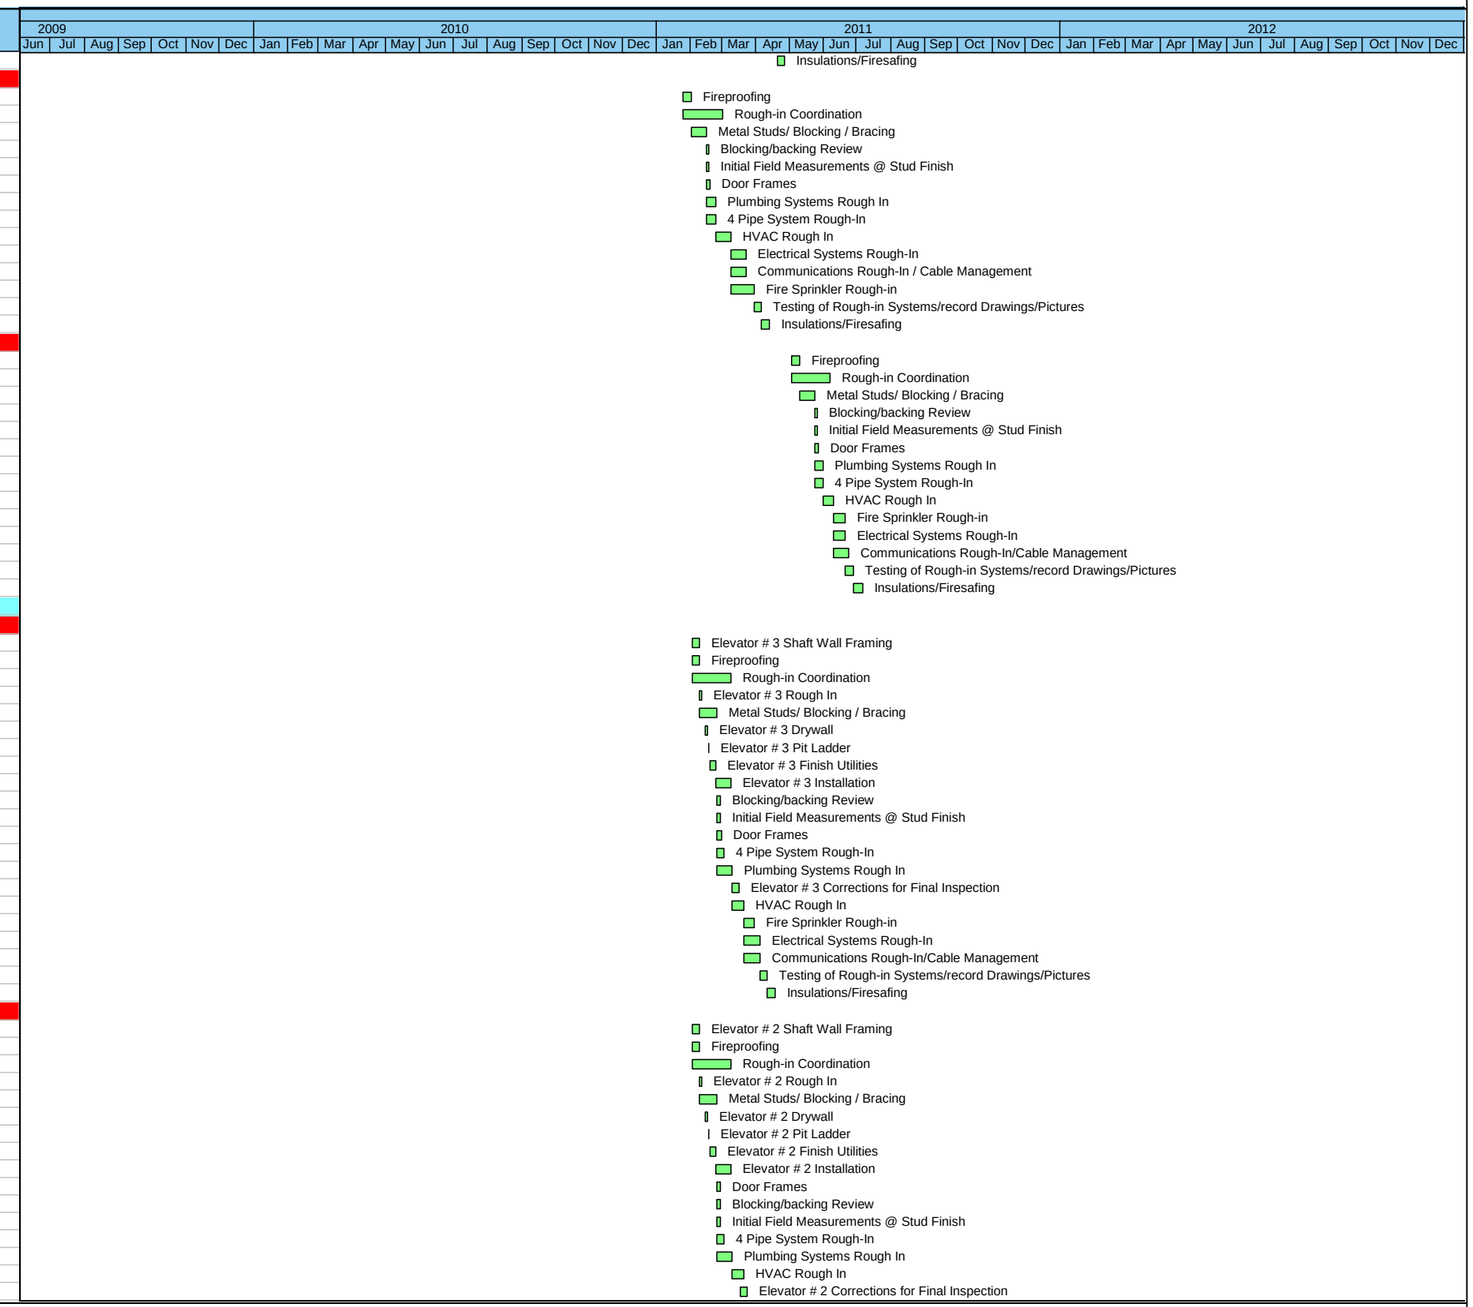

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

Klassen corporation

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
16070	Fire Sprinkler Rough-in	7	21-Mar-11	30-Mar-11
16090	Electrical Systems Rough-In	10	21-Mar-11	04-Apr-11
16290	Communications Rough-In / Cable Management	10	21-Mar-11	04-Apr-11
16110	Testing of Rough-in Systems/record Drawings/Pictures	5	04-Apr-11	11-Apr-11
16120	Insulations/Firesafing	5	11-Apr-11	18-Apr-11
South Wing		49	09-Feb-11	18-Apr-11
8290	Elevator # 1 Shaft Wall Framing	5	09-Feb-11	15-Feb-11
16160	Fireproofing	6	09-Feb-11	16-Feb-11
16170	Rough-in Coordination	25	09-Feb-11	16-Mar-11
8300	Elevator # 1 Rough In	3	16-Feb-11	18-Feb-11
16180	Metal Studs/ Blocking / Bracing	10	16-Feb-11	03-Mar-11
8310	Elevator # 1 Drywall	3	22-Feb-11	24-Feb-11
8320	Elevator # 1 Pit Ladder	1	25-Feb-11	25-Feb-11
8330	Elevator # 1 Finish Utilities	3	28-Feb-11	02-Mar-11
8340	Elevator # 1 Installation	10	03-Mar-11	16-Mar-11
16210	Door Frames	2	03-Mar-11	07-Mar-11
16220	Blocking/backing Review	2	03-Mar-11	07-Mar-11
16230	Initial Field Measurements @ Stud Finish	2	03-Mar-11	07-Mar-11
16190	Plumbing Systems Rough In	5	03-Mar-11	10-Mar-11
16200	4 Pipe System Rough-In	5	03-Mar-11	10-Mar-11
16250	HVAC Rough In	7	10-Mar-11	21-Mar-11
8350	Elevator # 1 Corrections for Final Inspection	5	18-Mar-11	24-Mar-11
16240	Fire Sprinkler Rough-in	7	21-Mar-11	30-Mar-11
16260	Electrical Systems Rough-In	10	21-Mar-11	04-Apr-11
16300	Communications Rough-In / Cable Management	10	21-Mar-11	04-Apr-11
16270	Testing of Rough-in Systems/record Drawings/Pictures	5	04-Apr-11	11-Apr-11
16280	Insulations/Firesafing	5	11-Apr-11	18-Apr-11
Planetarium		56	23-May-11	10-Aug-11
15600	Fireproofing	6	23-May-11	31-May-11
15620	Rough-In Coordination	25	23-May-11	27-Jun-11
15610	Metal Studs/ Blocking / Bracing	10	31-May-11	14-Jun-11
15700	Door Frames	2	14-Jun-11	16-Jun-11
15710	Blocking/backing Review	2	14-Jun-11	16-Jun-11
15720	Initial Field Measurements @ Stud Finish	2	14-Jun-11	16-Jun-11
15630	Plumbing Systems Rough In	5	14-Jun-11	21-Jun-11
15670	4 Pipe System Rough-In	5	14-Jun-11	21-Jun-11
15650	HVAC Rough In	10	21-Jun-11	06-Jul-11
15660	Electrical Systems Rough-In	5	06-Jul-11	13-Jul-11
15730	Communications Rough-In/ Cable Management	10	06-Jul-11	20-Jul-11
15640	Fire Sprinkler Rough-in	15	06-Jul-11	27-Jul-11
15680	Testing of Rough-in Systems/record Drawings/Pictures	5	27-Jul-11	03-Aug-11
15690	Insulations/Firesafing	5	03-Aug-11	10-Aug-11
Exterior Finishes / Curtain Wall Systems		196	02-Feb-11	07-Nov-11
East Wing		104	02-Feb-11	28-Jun-11
3750	Exterior Framing	10	02-Feb-11	15-Feb-11
3740	Exterior Insulation	5	16-Feb-11	23-Feb-11
2700	Exterior Wall Board	10	24-Feb-11	09-Mar-11
3640	Sheet Metal Work Needed Prior to Curtain Wall System and GFRC Panels	5	10-Mar-11	16-Mar-11
3650	GFRC Paneling	10	17-Mar-11	30-Mar-11
3700	Curtain Wall System Framework / Shade Devices	10	17-Mar-11	30-Mar-11
3790	Glazing Fabrication East Wing	25	31-Mar-11	04-May-11
3660	Glazing	10	05-May-11	18-May-11
3670	Metal Wall Panels/Sheet Metal Work	10	19-May-11	02-Jun-11
3690	Caulking/Sealants	3	03-Jun-11	07-Jun-11
3710	Exterior Railing/fabric/infill systems	15	08-Jun-11	28-Jun-11
North Wing		82	02-Feb-11	26-May-11
3620	Exterior Framing	10	02-Feb-11	15-Feb-11
5610	Exterior Wall Board	8	16-Feb-11	28-Feb-11
3630	Exterior Insulation	3	01-Mar-11	03-Mar-11
5620	Sheet Metal Work Needed Prior to Curtain Wall System and GFRC Panels	5	01-Mar-11	07-Mar-11
3610	Exterior Vapor Barrier	3	04-Mar-11	08-Mar-11
5630	GFRC Paneling	10	08-Mar-11	21-Mar-11
3800	Curtain Wall System Framework / Shade Devices	10	08-Mar-11	21-Mar-11
3810	Glazing Fabrication East Wing	20	22-Mar-11	18-Apr-11
5640	Glazing	15	19-Apr-11	09-May-11
5650	Metal Wall Panels/Sheet Metal Work	10	10-May-11	23-May-11
5660	Caulking/Sealants	3	24-May-11	26-May-11
South Wing		110	09-Feb-11	14-Jul-11
3030	Exterior Framing	10	09-Feb-11	23-Feb-11
5690	Exterior Wall Board	10	24-Feb-11	09-Mar-11

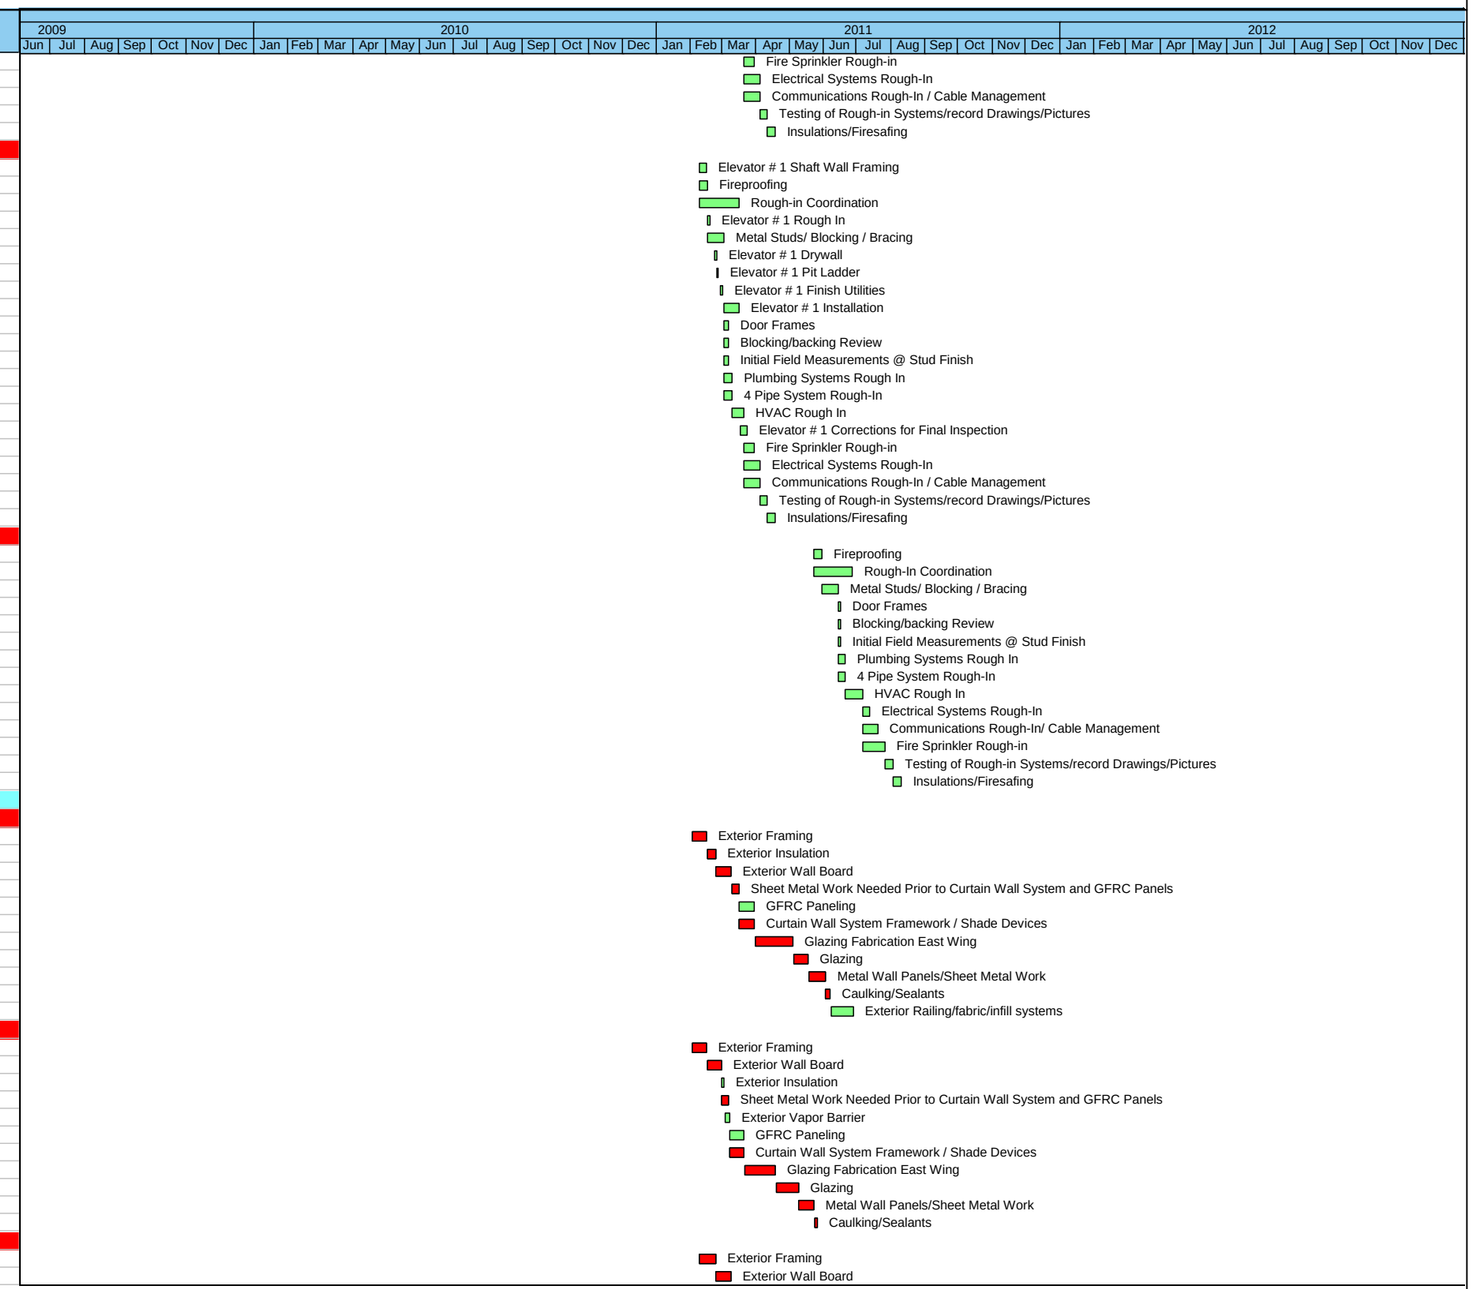

Actual Work
Remaining Work
Near Critical
Critical Remaining Work
◆ Milestone

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
3050	Exterior Vaper barrier	3	10-Mar-11	14-Mar-11
3040	Exterior Insulation	3	15-Mar-11	17-Mar-11
5700	Sheet Metal Work Needed Prior to Curtain Wall System and GFRC Panels	5	15-Mar-11	21-Mar-11
3820	Curtain Wall System Framework / Shade Devices	10	22-Mar-11	04-Apr-11
3830	Glazing Fabrication East Wing	20	05-Apr-11	02-May-11
5720	Glazing	20	03-May-11	31-May-11
5710	GFRC Paneling	8	01-Jun-11	10-Jun-11
5730	Metal Wall Panels/Sheet Metal Work	5	13-Jun-11	17-Jun-11
5740	Caulking/Sealants	3	20-Jun-11	22-Jun-11
5760	Exterior Railing/fabric/infill systems	15	23-Jun-11	14-Jul-11
Planetarium		118	23-May-11	07-Nov-11
3330	Exterior Framing	15	23-May-11	13-Jun-11
5770	Exterior Wall Board	5	14-Jun-11	20-Jun-11
3340	Exterior Vapor Barrier	3	21-Jun-11	23-Jun-11
3320	Exterior Insulation	3	24-Jun-11	28-Jun-11
5780	Sheet Metal Work Needed Prior to Curtain Wall System and GFRC Panels	5	24-Jun-11	30-Jun-11
3840	Curtain Wall System Framework / Shade Devices	10	01-Jul-11	15-Jul-11
3850	Glazing Fabrication East Wing	20	18-Jul-11	12-Aug-11
5800	Glazing	20	15-Aug-11	12-Sep-11
5790	GFRC Paneling	5	13-Sep-11	19-Sep-11
5810	Metal Wall Panels/Sheet Metal Work	10	20-Sep-11	03-Oct-11
5820	Caulking/Sealants	3	04-Oct-11	06-Oct-11
5830	Observations Deck Shade Devices	10	04-Oct-11	17-Oct-11
5840	Exterior Railing/fabric/infill systems	15	18-Oct-11	07-Nov-11
Finishes 1st Floor		244	15-Feb-11	31-Jan-12
East Wing		152	15-Feb-11	20-Sep-11
11340	Interior Aluminum Windows	8	15-Feb-11	28-Feb-11
12790	Interior Door Frames	8	15-Feb-11	28-Feb-11
11300	MEP Items Recessed in Drywall	10	13-Apr-11	27-Apr-11
2690	Drywall	15	08-Jun-11	28-Jun-11
2730	Final Field Measure after Drywall	3	29-Jun-11	01-Jul-11
10920	Painting	10	29-Jun-11	13-Jul-11
11110	Bathroom Tile	5	14-Jul-11	20-Jul-11
10940	Acoustical ceiling Framework	10	14-Jul-11	27-Jul-11
10990	Metal Ceiling Framework	10	14-Jul-11	27-Jul-11
11010	Casework	15	14-Jul-11	03-Aug-11
11120	Bathroom Plumbing Finish	5	21-Jul-11	27-Jul-11
11130	Bathroom Partitions	3	28-Jul-11	01-Aug-11
11000	Metal Ceiling Panels	5	28-Jul-11	03-Aug-11
11140	Bathroom Accessories	2	02-Aug-11	03-Aug-11
11150	Signage	3	04-Aug-11	08-Aug-11
10950	Acoustical Ceiling Tiles	5	04-Aug-11	10-Aug-11
11060	Lab Plumbing Finish	5	04-Aug-11	10-Aug-11
11070	Lab Equipment	5	04-Aug-11	10-Aug-11
11020	Plumbing Rough-In at Casework	7	04-Aug-11	12-Aug-11
11190	Doors & Hardware	8	04-Aug-11	15-Aug-11
11210	Finish Electrical Systems	10	04-Aug-11	17-Aug-11
11330	Finish Flooring	15	04-Aug-11	24-Aug-11
10960	HVAC Ceiling Finish	5	11-Aug-11	17-Aug-11
11080	Lab Equipment Plumbing	7	11-Aug-11	19-Aug-11
11040	Electrical Rough-in at Casework	4	15-Aug-11	18-Aug-11
11030	Casework Plumbing Finish	5	15-Aug-11	19-Aug-11
10970	Fire Sprinkler ceiling Finish	5	18-Aug-11	24-Aug-11
11220	Finish Audio Visual	5	18-Aug-11	24-Aug-11
11100	Lab Equipment HVAC	2	22-Aug-11	23-Aug-11
11050	Casework Electrical Finish	3	22-Aug-11	24-Aug-11
11090	Lab Equipment Electrical	3	24-Aug-11	26-Aug-11
11950	Tech Racks	3	25-Aug-11	29-Aug-11
10980	Electrical Systems Ceiling Finish	5	25-Aug-11	31-Aug-11
11230	Finish Fire Alarm	5	25-Aug-11	31-Aug-11
11960	Tech Equipment	3	30-Aug-11	01-Sep-11
11970	Tech Terminations/Testing	5	02-Sep-11	09-Sep-11
11320	Touch Up Painting	4	12-Sep-11	15-Sep-11
11310	Final Cleanup/Polishing	3	16-Sep-11	20-Sep-11*
North Wing		136	15-Feb-11	26-Aug-11
10880	Interior Aluminum Windows	10	15-Feb-11	02-Mar-11
11250	Interior Door Frames	10	15-Feb-11	02-Mar-11
10870	MEP Items Recessed in Drywall	10	20-Apr-11	04-May-11
4920	Drywall	15	27-May-11	17-Jun-11
10500	Plywood at Electrical Room	1	20-Jun-11	20-Jun-11

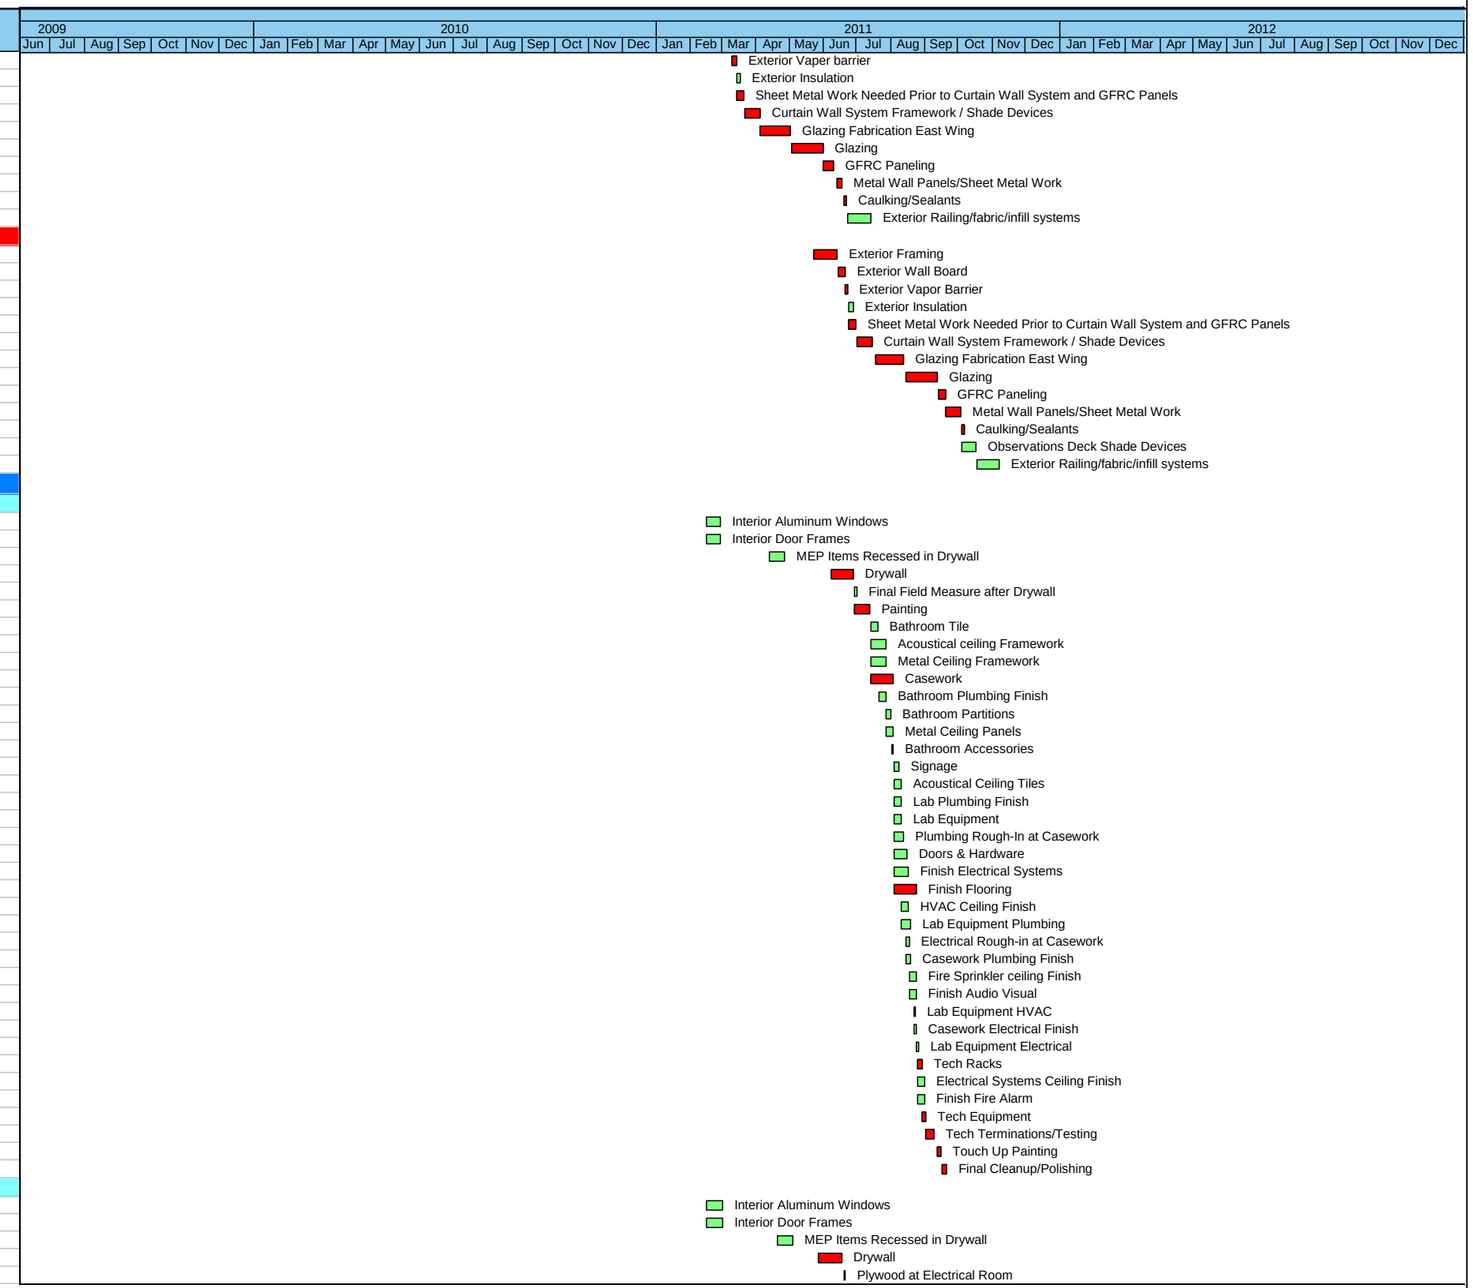

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
2640	Food Service Field Measurement	2	20-Jun-11	21-Jun-11
4930	Final Field Measure after Drywall	2	20-Jun-11	21-Jun-11
10580	Plumbing Equipment at Pads	5	20-Jun-11	24-Jun-11
12170	Tile	5	20-Jun-11	24-Jun-11
11980	Painting	10	20-Jun-11	01-Jul-11
12260	Finish Plumbing	10	20-Jun-11	01-Jul-11
10510	Paint at Electrical Room	3	21-Jun-11	23-Jun-11
10470	Food Service Stainless Work	5	22-Jun-11	28-Jun-11
10520	Floor Sealer at electrical room	3	24-Jun-11	28-Jun-11
10590	Finish Flooring in Plumbing Equipment Room	3	27-Jun-11	29-Jun-11
10480	Food Service MEP	5	29-Jun-11	06-Jul-11
10530	Electrical Panels/ Equipment	7	29-Jun-11	08-Jul-11
10600	Plumbing Equipment @ equipment room	5	30-Jun-11	07-Jul-11
12000	Acoustical ceiling Framework	5	05-Jul-11	11-Jul-11
12050	Metal Ceiling Framework	5	05-Jul-11	11-Jul-11
12290	Finish Fire Alarm	5	05-Jul-11	11-Jul-11
12070	Casework	10	05-Jul-11	18-Jul-11
12270	Finish Electrical	10	05-Jul-11	18-Jul-11
12280	Finish Audio Visual	10	05-Jul-11	18-Jul-11
10490	Food Service Equipment	10	07-Jul-11	20-Jul-11
10610	Final MEP work at equipment room	10	08-Jul-11	21-Jul-11
10540	Conduit/Boxes at Equipment Rooms	3	11-Jul-11	13-Jul-11
12010	Acoustical Ceiling Tiles	5	12-Jul-11	18-Jul-11
12060	Metal Ceiling Panels	5	12-Jul-11	18-Jul-11
12020	HVAC Ceiling Finish	10	12-Jul-11	25-Jul-11
10550	Feeders	3	14-Jul-11	18-Jul-11
12100	Electrical Rough-in at Casework	3	19-Jul-11	21-Jul-11
10900	Woven Wire Mesh	4	19-Jul-11	22-Jul-11
12120	Lab Plumbing Finish	4	19-Jul-11	22-Jul-11
12080	Plumbing Rough-In at Casework	5	19-Jul-11	25-Jul-11
12130	Lab Equipment	5	19-Jul-11	25-Jul-11
12250	Doors & Hardware	8	19-Jul-11	28-Jul-11
12490	Finish Flooring	10	19-Jul-11	01-Aug-11
12030	Fire Sprinkler ceiling Finish	4	26-Jul-11	29-Jul-11
12090	Casework Plumbing Finish	5	26-Jul-11	01-Aug-11
12140	Lab Equipment Plumbing	5	26-Jul-11	01-Aug-11
12210	Signage	2	29-Jul-11	01-Aug-11
12040	Electrical Systems Ceiling Finish	5	01-Aug-11	05-Aug-11
12110	Casework Electrical Finish	5	02-Aug-11	08-Aug-11
12160	Lab Equipment HVAC	5	02-Aug-11	08-Aug-11
12150	Lab Equipment Electrical	5	09-Aug-11	15-Aug-11
10560	Labeling/testing/startup	3	16-Aug-11	18-Aug-11
10570	Paint Touch Up	3	19-Aug-11	23-Aug-11
10890	Final Cleanup/Polishing	3	24-Aug-11	26-Aug-11*
South Wing		179	15-Feb-11	27-Oct-11
11510	Interior Aluminum Windows	8	15-Feb-11	28-Feb-11
12800	Interior Door Frames	8	15-Feb-11	28-Feb-11
11500	MEP Items Recessed in Drywall	10	06-Apr-11	20-Apr-11
5680	Drywall	15	23-Jun-11	14-Jul-11
5750	Final Field Measure after Drywall	3	15-Jul-11	19-Jul-11
10930	Painting	10	15-Jul-11	28-Jul-11
10060	Headwalls	2	29-Jul-11	01-Aug-11
10080	Perforated Metal Ceiling Framing	5	29-Jul-11	04-Aug-11
11180	Bathroom Tile	5	29-Jul-11	04-Aug-11
11160	Acoustical ceiling Framework	10	29-Jul-11	11-Aug-11
11170	Metal Ceiling Framework	10	29-Jul-11	11-Aug-11
10090	Perforated Metal Ceiling Panels	5	05-Aug-11	11-Aug-11
11200	Bathroom Plumbing Finish	5	05-Aug-11	11-Aug-11
11530	Bathroom Partitions	3	12-Aug-11	16-Aug-11
10070	Curtain Track System	4	12-Aug-11	17-Aug-11
10100	MEP at Perforated Metal Ceilings	5	12-Aug-11	18-Aug-11
11520	Metal Ceiling Panels	5	12-Aug-11	18-Aug-11
11560	Casework	15	12-Aug-11	01-Sep-11
11540	Bathroom Accessories	2	17-Aug-11	18-Aug-11
11550	Signage	3	19-Aug-11	23-Aug-11
11570	Acoustical Ceiling Tiles	5	02-Sep-11	09-Sep-11
11720	Doors	5	02-Sep-11	09-Sep-11
11580	Plumbing Rough-In at Casework	7	02-Sep-11	13-Sep-11
11730	Finish Electrical Systems	10	02-Sep-11	16-Sep-11
11990	Finish Flooring	15	02-Sep-11	23-Sep-11
10030	Acoustical Wall Panels	3	12-Sep-11	14-Sep-11

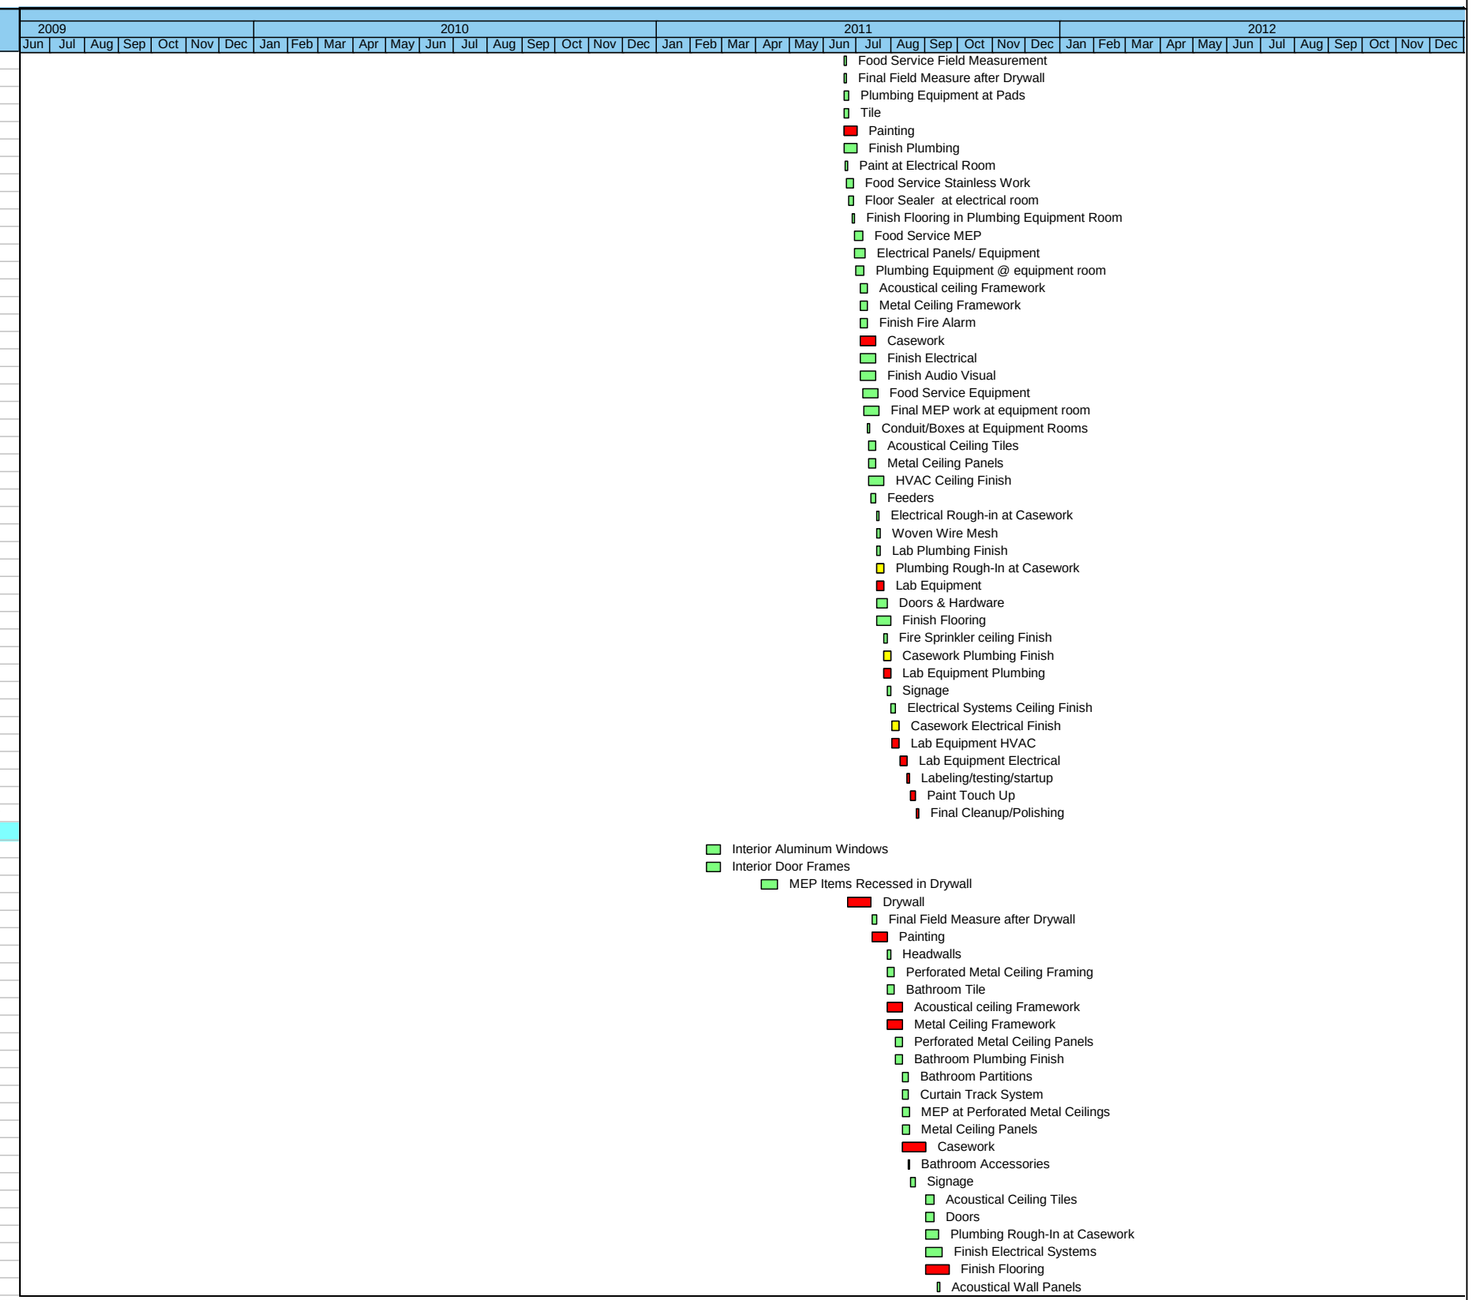

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
10460	Painting at Doors	4	12-Sep-11	15-Sep-11
12180	HVAC Ceiling Finish	5	12-Sep-11	16-Sep-11
12220	Electrical Rough-in at Casework	4	14-Sep-11	19-Sep-11
11590	Casework Plumbing Finish	5	14-Sep-11	20-Sep-11
10040	Tackable Wall Panels	3	15-Sep-11	19-Sep-11
10450	Door Hardware/Balancing	5	16-Sep-11	22-Sep-11
12230	Fire Sprinkler ceiling Finish	5	19-Sep-11	23-Sep-11
12240	Finish Audio Visual	10	19-Sep-11	30-Sep-11
13390	Casework Electrical Finish	3	20-Sep-11	22-Sep-11
10050	Marker/Tack Boards	4	20-Sep-11	23-Sep-11
13510	Electrical Systems Ceiling Finish	5	26-Sep-11	30-Sep-11
11920	Tech Racks	5	26-Sep-11	30-Sep-11
13520	Finish Fire Alarm	5	03-Oct-11	07-Oct-11
11930	Tech Equipment	5	03-Oct-11	07-Oct-11
11940	Tech Terminations/Testing	7	10-Oct-11	18-Oct-11
13530	Touch Up Painting	4	19-Oct-11	24-Oct-11
13540	Final Cleanup/Polishing	3	25-Oct-11	27-Oct-11*
Planetarium		174	24-May-11	31-Jan-12
12190	Interior Aluminum Windows	8	24-May-11	06-Jun-11
12810	Interior Door Frames	8	24-May-11	06-Jun-11
11710	MEP Items Recessed in Drywall	10	28-Jun-11	13-Jul-11
5850	Drywall	15	07-Oct-11	27-Oct-11
5860	Final Field Measure after Drywall	3	28-Oct-11	01-Nov-11
12200	Painting	10	28-Oct-11	10-Nov-11
13550	Bathroom Tile	5	14-Nov-11	18-Nov-11
13440	Acoustical ceiling Framework	10	14-Nov-11	29-Nov-11
13500	Metal Ceiling Framework	10	14-Nov-11	29-Nov-11
13610	Casework	15	14-Nov-11	06-Dec-11
13560	Bathroom Plumbing Finish	5	21-Nov-11	29-Nov-11
13580	Bathroom Partitions	3	30-Nov-11	02-Dec-11
13570	Metal Ceiling Panels	5	30-Nov-11	06-Dec-11
13590	Bathroom Accessories	2	05-Dec-11	06-Dec-11
13600	Signage	3	07-Dec-11	09-Dec-11
13620	Acoustical Ceiling Tiles	5	07-Dec-11	13-Dec-11
13630	Plumbing Rough-In at Casework	7	07-Dec-11	15-Dec-11
13660	Doors & Hardware	8	07-Dec-11	16-Dec-11
13670	Finish Electrical Systems	10	07-Dec-11	20-Dec-11
13680	Finish Flooring	15	07-Dec-11	05-Jan-12
13690	HVAC Ceiling Finish	5	14-Dec-11	20-Dec-11
13720	Electrical Rough-in at Casework	4	16-Dec-11	21-Dec-11
13710	Casework Plumbing Finish	5	16-Dec-11	22-Dec-11
13730	Fire Sprinkler ceiling Finish	5	21-Dec-11	05-Jan-12
13740	Finish Audio Visual	5	21-Dec-11	05-Jan-12
13750	Casework Electrical Finish	3	03-Jan-12	05-Jan-12
13780	Electrical Systems Ceiling Finish	5	06-Jan-12	12-Jan-12
13790	Finish Fire Alarm	5	06-Jan-12	12-Jan-12
7840	Planetarium Seating	15	06-Jan-12	26-Jan-12
13800	Touch Up Painting	4	13-Jan-12	18-Jan-12
13810	Final Cleanup/Polishing	3	27-Jan-12	31-Jan-12*
Finishes 2nd Floor		231	24-Feb-11	23-Jan-12
East Wing		151	24-Feb-11	28-Sep-11
13830	Interior Aluminum Windows	8	24-Feb-11	08-Mar-11
15020	Interior Door Frames	8	24-Feb-11	08-Mar-11
13820	MEP Items Recessed in Drywall	10	11-Apr-11	25-Apr-11
5870	Drywall	15	08-Jun-11	28-Jun-11
5880	Final Field Measure after Drywall	3	29-Jun-11	01-Jul-11
13840	Painting	10	29-Jun-11	13-Jul-11
13870	Bathroom Tile	5	14-Jul-11	20-Jul-11
14960	Railing System	5	14-Jul-11	20-Jul-11
13850	Acoustical ceiling Framework	10	14-Jul-11	27-Jul-11
13860	Metal Ceiling Framework	10	14-Jul-11	27-Jul-11
13930	Casework	15	14-Jul-11	03-Aug-11
13880	Bathroom Plumbing Finish	5	21-Jul-11	27-Jul-11
13900	Bathroom Partitions	3	28-Jul-11	01-Aug-11
13890	Metal Ceiling Panels	5	28-Jul-11	03-Aug-11
13910	Bathroom Accessories	2	02-Aug-11	03-Aug-11
13920	Signage	3	04-Aug-11	08-Aug-11
13940	Acoustical Ceiling Tiles	5	04-Aug-11	10-Aug-11
13960	Lab Plumbing Finish	5	04-Aug-11	10-Aug-11
13970	Lab Equipment	5	04-Aug-11	10-Aug-11
13950	Plumbing Rough-In at Casework	7	04-Aug-11	12-Aug-11

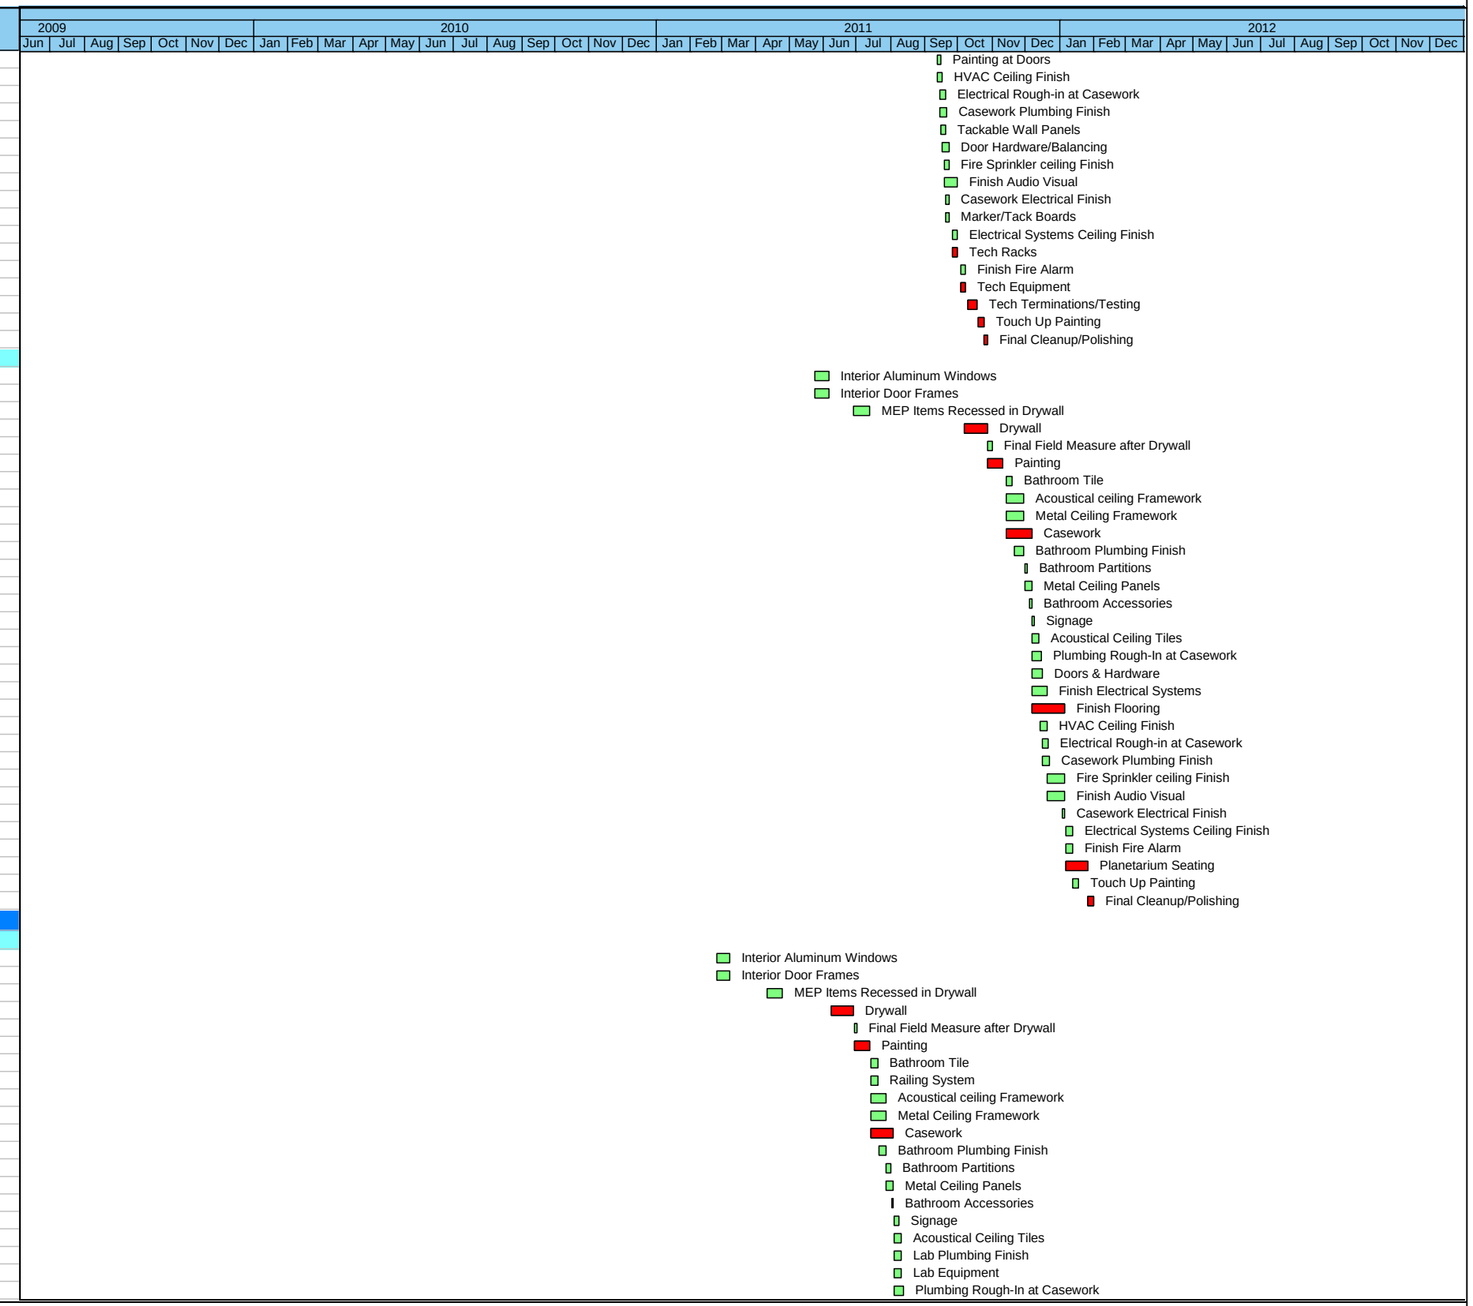

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
13980	Doors & Hardware	8	04-Aug-11	15-Aug-11
13990	Finish Electrical Systems	10	04-Aug-11	17-Aug-11
14000	Finish Flooring	15	04-Aug-11	24-Aug-11
14010	HVAC Ceiling Finish	5	11-Aug-11	17-Aug-11
14020	Lab Equipment Plumbing	7	11-Aug-11	19-Aug-11
14040	Electrical Rough-in at Casework	4	15-Aug-11	18-Aug-11
14030	Casework Plumbing Finish	5	15-Aug-11	19-Aug-11
14050	Fire Sprinkler ceiling Finish	5	18-Aug-11	24-Aug-11
14060	Finish Audio Visual	5	18-Aug-11	24-Aug-11
14080	Lab Equipment HVAC	2	22-Aug-11	23-Aug-11
14070	Casework Electrical Finish	3	22-Aug-11	24-Aug-11
14090	Lab Equipment Electrical	3	24-Aug-11	26-Aug-11
14100	Electrical Systems Ceiling Finish	5	25-Aug-11	31-Aug-11
14110	Finish Fire Alarm	5	25-Aug-11	31-Aug-11
12560	Tech Racks	5	25-Aug-11	31-Aug-11
12680	Tech Equipment	5	01-Sep-11	08-Sep-11
12690	Tech Terminations/Testing	7	09-Sep-11	19-Sep-11
14120	Touch Up Painting	4	20-Sep-11	23-Sep-11
14130	Final Cleanup/Polishing	3	26-Sep-11	28-Sep-11*
North Wing		125	24-Feb-11	22-Aug-11
14510	Interior Aluminum Windows	10	24-Feb-11	10-Mar-11
15080	Interior Door Frames	10	24-Feb-11	10-Mar-11
14520	MEP Items Recessed in Drywall	10	11-Apr-11	25-Apr-11
5910	Drywall	15	27-May-11	17-Jun-11
5920	Final Field Measure after Drywall	2	20-Jun-11	21-Jun-11
14710	Final MEP work at equipment room	5	20-Jun-11	24-Jun-11
14560	Tile	5	20-Jun-11	24-Jun-11
14550	Painting	10	20-Jun-11	01-Jul-11
14570	Finish Plumbing	10	20-Jun-11	01-Jul-11
14640	Finish Fire Alarm	5	05-Jul-11	11-Jul-11
14680	Acoustical ceiling Framework	10	05-Jul-11	18-Jul-11
14690	Metal Ceiling Framework	10	05-Jul-11	18-Jul-11
14700	Casework	10	05-Jul-11	18-Jul-11
14620	Finish Electrical	10	05-Jul-11	18-Jul-11
14630	Finish Audio Visual	10	05-Jul-11	18-Jul-11
14970	Railing Systems	10	05-Jul-11	18-Jul-11
14790	Electrical Rough-in at Casework	3	19-Jul-11	21-Jul-11
14740	Woven Wire Mesh	4	19-Jul-11	22-Jul-11
14800	Lab Plumbing Finish	4	19-Jul-11	22-Jul-11
14750	Acoustical Ceiling Tiles	5	19-Jul-11	25-Jul-11
14770	Metal Ceiling Panels	5	19-Jul-11	25-Jul-11
14780	Plumbing Rough-In at Casework	5	19-Jul-11	25-Jul-11
14810	Lab Equipment	5	19-Jul-11	25-Jul-11
14820	Doors & Hardware	8	19-Jul-11	28-Jul-11
14760	HVAC Ceiling Finish	10	19-Jul-11	01-Aug-11
14840	Lab Equipment Plumbing	3	26-Jul-11	28-Jul-11
14850	Casework Plumbing Finish	5	26-Jul-11	01-Aug-11
14870	Signage	2	29-Jul-11	01-Aug-11
14860	Lab Equipment HVAC	5	29-Jul-11	04-Aug-11
14880	Fire Sprinkler ceiling Finish	4	02-Aug-11	05-Aug-11
14890	Casework Electrical Finish	5	02-Aug-11	08-Aug-11
14900	Lab Equipment Electrical	5	05-Aug-11	11-Aug-11
14910	Electrical Systems Ceiling Finish	5	08-Aug-11	12-Aug-11
14930	Paint Touch Up	3	15-Aug-11	17-Aug-11
14940	Final Cleanup/Polishing	3	18-Aug-11	22-Aug-11*
South Wing		167	03-Mar-11	27-Oct-11
14150	Interior Aluminum Windows	8	03-Mar-11	15-Mar-11
15090	Interior Door Frames	8	03-Mar-11	15-Mar-11
15340	ICU Sliding Door Frames	1	15-Mar-11	16-Mar-11
14140	MEP Items Recessed in Drywall	10	11-Apr-11	25-Apr-11
5890	Drywall	15	23-Jun-11	14-Jul-11
5900	Final Field Measure after Drywall	3	15-Jul-11	19-Jul-11
14160	Painting	10	15-Jul-11	28-Jul-11
10910	Headwalls	3	29-Jul-11	02-Aug-11
14170	Perforated Metal Ceiling Framing	5	29-Jul-11	04-Aug-11
14200	Bathroom Tile	5	29-Jul-11	04-Aug-11
11240	Railing Systems	5	29-Jul-11	04-Aug-11
14180	Acoustical ceiling Framework	10	29-Jul-11	11-Aug-11
14190	Metal Ceiling Framework	10	29-Jul-11	11-Aug-11
14210	Perforated Metal Ceiling Panels	3	05-Aug-11	09-Aug-11
14220	Bathroom Plumbing Finish	5	05-Aug-11	11-Aug-11

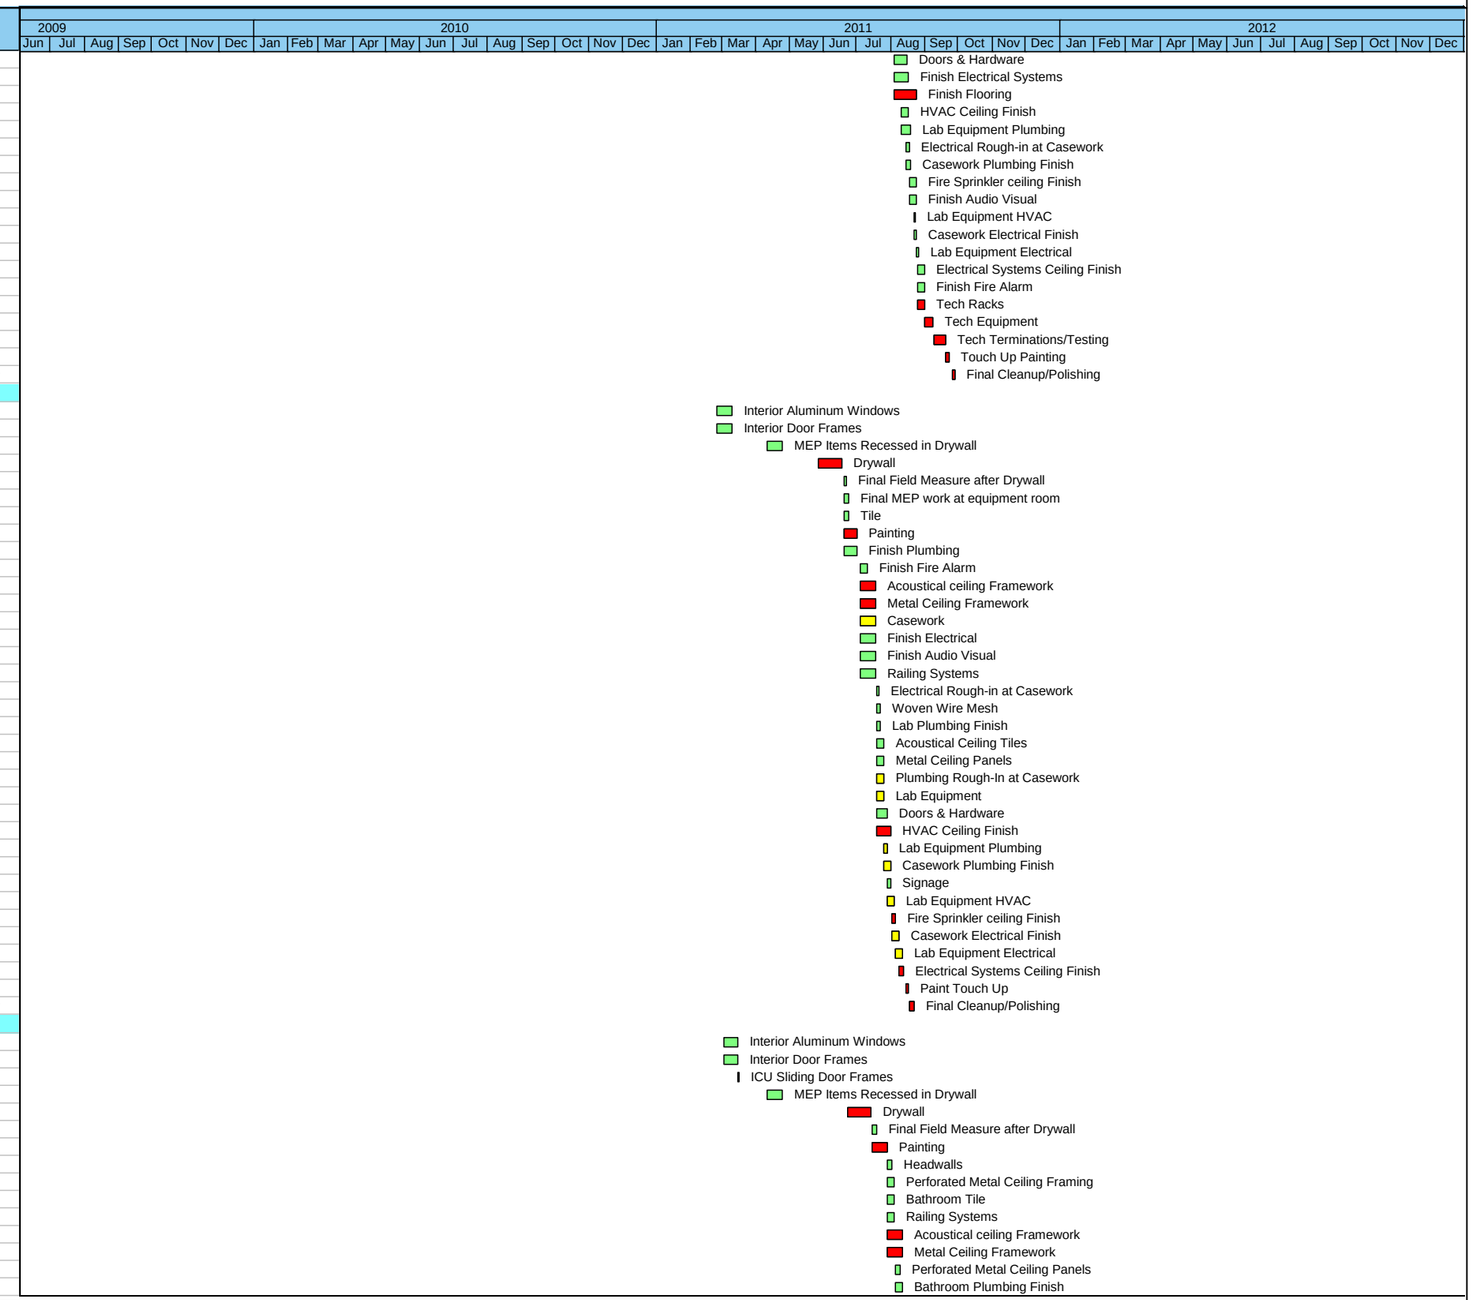

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
14230	MEP at Perforated Metal Ceilings	4	10-Aug-11	15-Aug-11
14270	Bathroom Partitions	3	12-Aug-11	16-Aug-11
14240	Curtain Track System	5	12-Aug-11	18-Aug-11
14250	Metal Ceiling Panels	5	12-Aug-11	18-Aug-11
14260	Casework	15	12-Aug-11	01-Sep-11
14280	Bathroom Accessories	2	17-Aug-11	18-Aug-11
14290	Signage	3	19-Aug-11	23-Aug-11
15350	ICU Sliding Doors	1	02-Sep-11	02-Sep-11
14300	Acoustical Ceiling Tiles	5	02-Sep-11	09-Sep-11
14320	Doors	5	02-Sep-11	09-Sep-11
14310	Plumbing Rough-In at Casework	7	02-Sep-11	13-Sep-11
14330	Finish Electrical Systems	10	02-Sep-11	16-Sep-11
14340	Finish Flooring	15	02-Sep-11	23-Sep-11
14350	Acoustical Wall Panels	3	12-Sep-11	14-Sep-11
14360	Painting at Doors	4	12-Sep-11	15-Sep-11
14370	HVAC Ceiling Finish	5	12-Sep-11	16-Sep-11
14380	Electrical Rough-in at Casework	4	14-Sep-11	19-Sep-11
14390	Casework Plumbing Finish	5	14-Sep-11	20-Sep-11
14400	Tackable Wall Panels	3	15-Sep-11	19-Sep-11
14410	Door Hardware/Balancing	5	16-Sep-11	22-Sep-11
14420	Fire Sprinkler ceiling Finish	5	19-Sep-11	23-Sep-11
14430	Finish Audio Visual	5	19-Sep-11	23-Sep-11
14450	Casework Electrical Finish	3	20-Sep-11	22-Sep-11
14440	Marker/Tack Boards	4	20-Sep-11	23-Sep-11
14470	Electrical Systems Ceiling Finish	5	26-Sep-11	30-Sep-11
14480	Finish Fire Alarm	5	26-Sep-11	30-Sep-11
12700	Tech Racks	5	26-Sep-11	30-Sep-11
14460	Lecture Hall Seating	15	26-Sep-11	14-Oct-11
12710	Tech Equipment	5	03-Oct-11	07-Oct-11
12720	Tech Terminations/Testing	7	10-Oct-11	18-Oct-11
14490	Touch Up Painting	4	19-Oct-11	24-Oct-11
14500	Final Cleanup/Polishing	3	25-Oct-11	27-Oct-11*
Planetarium		168	24-May-11	23-Jan-12
2530	Planetarium Framing	15	24-May-11	15-Jun-11
14540	Interior Aluminum Windows	8	14-Jun-11	24-Jun-11
15330	Interior Door Frames	8	14-Jun-11	24-Jun-11
7870	Planetarium Cove Trough System	5	15-Jun-11	22-Jun-11
7820	Planetarium Panels	10	15-Jun-11	29-Jun-11
7850	Catwalk	10	15-Jun-11	29-Jun-11
7860	Cat Walk Handrailing	5	29-Jun-11	07-Jul-11
7830	Planetarium Finish Coating	8	29-Jun-11	12-Jul-11
14530	MEP Items Recessed in Drywall	10	03-Aug-11	17-Aug-11
5930	Drywall	15	07-Oct-11	27-Oct-11
5940	Final Field Measure after Drywall	3	28-Oct-11	01-Nov-11
14580	Painting	10	28-Oct-11	10-Nov-11
14720	Bathroom Accessories	2	14-Nov-11	15-Nov-11
14590	Acoustical ceiling Framework	10	14-Nov-11	29-Nov-11
14600	Metal Ceiling Framework	10	14-Nov-11	29-Nov-11
14830	Casework	15	14-Nov-11	06-Dec-11
14660	Metal Ceiling Panels	5	30-Nov-11	06-Dec-11
2840	Observation Deck Waterproofing	2	07-Dec-11	08-Dec-11
14730	Signage	3	07-Dec-11	09-Dec-11
14920	Acoustical Ceiling Tiles	5	07-Dec-11	13-Dec-11
14950	Plumbing Rough-In at Casework	7	07-Dec-11	15-Dec-11
14980	Doors & Hardware	8	07-Dec-11	16-Dec-11
14990	Finish Electrical Systems	10	07-Dec-11	20-Dec-11
15000	Finish Flooring	15	07-Dec-11	05-Jan-12
2850	Observation Deck Lithocrete	5	09-Dec-11	15-Dec-11
15010	HVAC Ceiling Finish	5	14-Dec-11	20-Dec-11
15040	Electrical Rough-in at Casework	4	16-Dec-11	21-Dec-11
15030	Casework Plumbing Finish	5	16-Dec-11	22-Dec-11
2860	Railing Systems	10	16-Dec-11	09-Jan-12
15050	Fire Sprinkler ceiling Finish	5	21-Dec-11	05-Jan-12
15060	Finish Audio Visual	5	21-Dec-11	05-Jan-12
15070	Casework Electrical Finish	3	03-Jan-12	05-Jan-12
15100	Electrical Systems Ceiling Finish	5	06-Jan-12	12-Jan-12
15110	Finish Fire Alarm	5	06-Jan-12	12-Jan-12
15120	Touch Up Painting	4	13-Jan-12	18-Jan-12
15130	Final Cleanup/Polishing	3	19-Jan-12	23-Jan-12*
Roof		85	04-Feb-11	03-Jun-11
11350	Elevator / Parapet / Standing SeamFraming	10	04-Feb-11	17-Feb-11

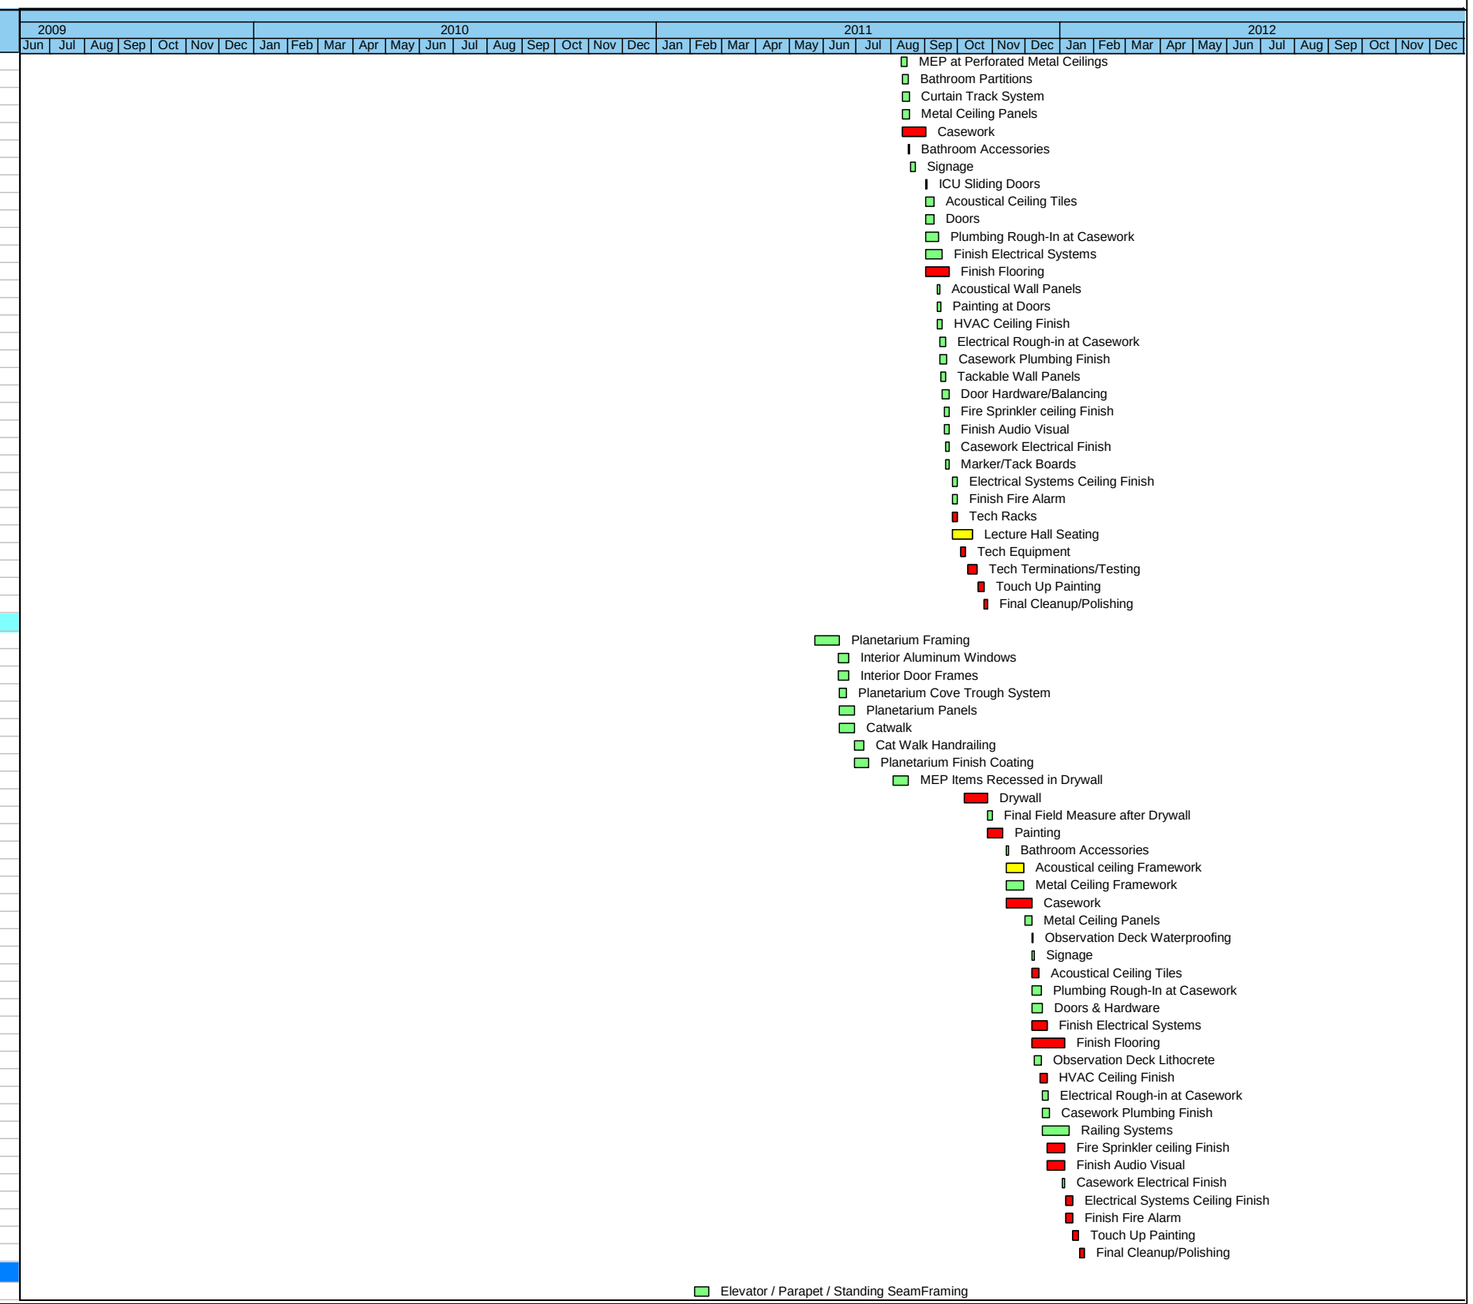

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work

AVC Health Science Building

Baseline Construction Schedule

Activity ID	Activity Name	Original Duration	Start	Finish
11460	Door Frames	2	18-Feb-11	22-Feb-11
13770	Field Measure Standing Seam Roofing	2	18-Feb-11	22-Feb-11
11400	Wall Insulation	3	18-Feb-11	23-Feb-11
11360	Roof Penetrations/Flashing	15	18-Feb-11	11-Mar-11
11470	Doors	1	23-Feb-11	23-Feb-11
11480	Paint	2	24-Feb-11	25-Feb-11
11490	Plaster	10	28-Feb-11	11-Mar-11
11370	Mechanical Curbs	4	14-Mar-11	17-Mar-11
11380	Wood Nailers and Plywood	6	18-Mar-11	25-Mar-11
11390	Underlayment Board	2	28-Mar-11	29-Mar-11
11410	Roof Insulation	10	30-Mar-11	12-Apr-11
11420	Tapered Insulation	10	13-Apr-11	26-Apr-11
12730	Standing Seam Vapor Retarder	3	27-Apr-11	29-Apr-11
11430	Single Ply Roofing	15	27-Apr-11	17-May-11
12740	Standing Seam Clips	5	02-May-11	06-May-11
12750	Standing Seam Insulation	3	09-May-11	11-May-11
12760	Standing Seam Panels	10	12-May-11	25-May-11
11440	Roof Equipement	7	18-May-11	26-May-11
12770	Standing Seam Flashing/Trim	3	26-May-11	31-May-11
11450	Coping/Flashing	5	27-May-11	03-Jun-11
Post-Construction Phase		382	07-Feb-11	01-Aug-12
CM Construction Services		73	23-Jan-12	03-May-12
6310	Hardware Training	1	23-Jan-12	24-Jan-12
6320	Lab Equipment Training	1	23-Jan-12	24-Jan-12
6330	Fire Alarm Training	1	23-Jan-12	24-Jan-12
6340	Hydraulic Elevator Training	1	23-Jan-12	24-Jan-12
6350	Reverse Osmosis Water System Training	1	23-Jan-12	24-Jan-12
6360	Heating Boilers and Accessories Training	1	23-Jan-12	24-Jan-12
6370	Air Handling Unit Training	1	23-Jan-12	24-Jan-12
6380	VFD Training	1	23-Jan-12	24-Jan-12
6390	DDC Training	1	23-Jan-12	24-Jan-12
6400	Engine Generator Training	1	23-Jan-12	24-Jan-12
6410	Pad Mounted Transformer Training	1	23-Jan-12	24-Jan-12
6420	Automatic Transfer Switch Training	1	23-Jan-12	24-Jan-12
6260	O&M Manuals	30	23-Jan-12	05-Mar-12
6300	Irrigation System Training	1	21-Mar-12	22-Mar-12
6270	As-Builts	15	21-Mar-12	11-Apr-12
6290	Closeout Documents	30	21-Mar-12	02-May-12
6280	As-Built review/Approval	15	11-Apr-12	02-May-12
2440	Final Construction Billing	1	02-May-12	03-May-12
Post Construction		382	07-Feb-11	01-Aug-12
Post Construction Without Weather Delays		337	07-Feb-11	30-May-12
2130	Campus Request Funds for FF&E (50% of Construction)	10	07-Feb-11*	18-Feb-11
2140	Campus FF&E Fabrication	60	21-Feb-11	13-May-11
9580	DSA Final Inspection	5	10-Feb-12	17-Feb-12
2660	Training	20	13-Feb-12	12-Mar-12
2590	Punch List Creation	15	29-Feb-12	21-Mar-12
2610	Contractor Punch List Corrections	20	21-Mar-12	18-Apr-12
2620	Final Walk for Acceptance of Site	5	18-Apr-12	25-Apr-12
2750	Campus FF&E Installation	25	25-Apr-12	30-May-12
Post Construction With Forecasted Weather Delays		123	10-Feb-12	01-Aug-12
2630	Weather Days (24 per year)	48	10-Feb-12	18-Apr-12
9590	DSA Final Inspection	5	18-Apr-12	25-Apr-12
2910	Punch List Creation	15	18-Apr-12	09-May-12
2900	Training	20	18-Apr-12	16-May-12
2920	Contractor Punch List Corrections	20	09-May-12	06-Jun-12
2930	Final Walk for Acceptance of Site	5	06-Jun-12	13-Jun-12
2940	Campus FF&E Installation	25	13-Jun-12	18-Jul-12
2380	Owner Move-In Including Forecasted Weather Delays	10	18-Jul-12	01-Aug-12

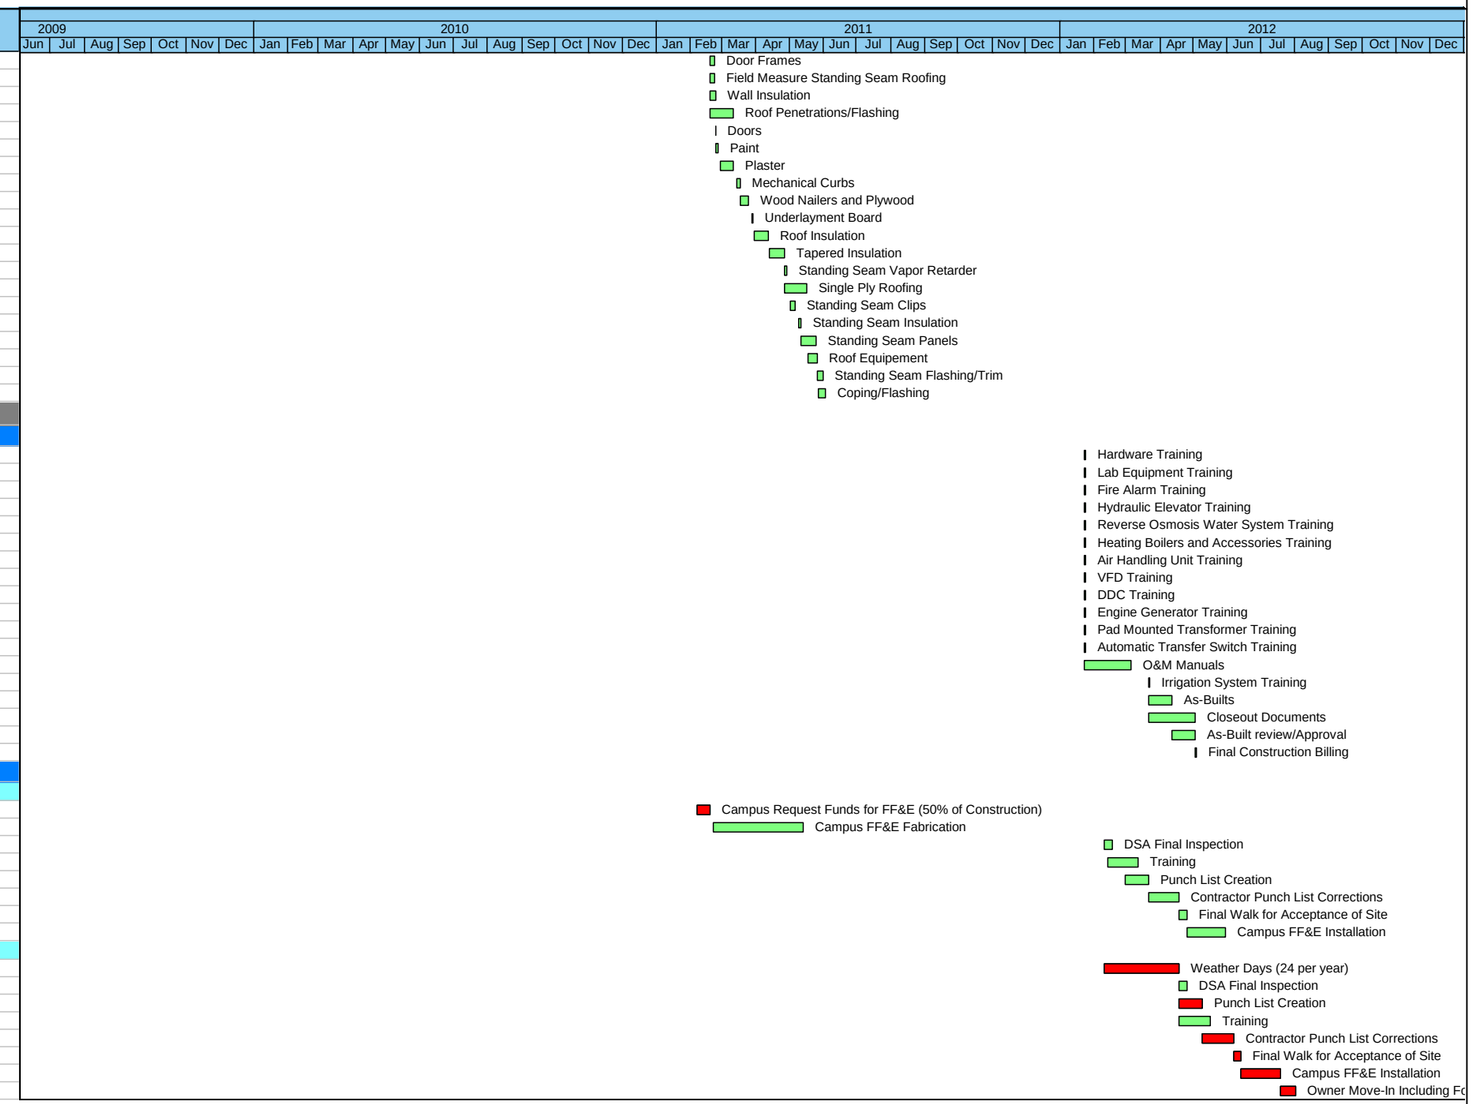

Actual Work | Near Critical | ◆ Milestone
Remaining Work | Critical Remaining Work
